

**2021 BOND PROGRAM  
CONSTRUCTION UPDATE**

---

**GALESBURG-AUGUSTA COMMUNITY SCHOOLS  
HIGH SCHOOL MULTI-PURPOSE ADDITION &  
WEIGHTROOM**

**1/2/2024**



# MULTI-PURPOSE OVERVIEW





# MULTI-PURPOSE OVERVIEW



- Steel joist & deck underway.
- Start metal panel framing for soffit & fascia details.




# ROBOTICS ROOM OVERVIEW



- Structural steel 95% complete
- Decking to start tomorrow (1/3/24).
- Continue masonry at multi-purpose storage room.



# WEIGHT ROOM OVERVIEW

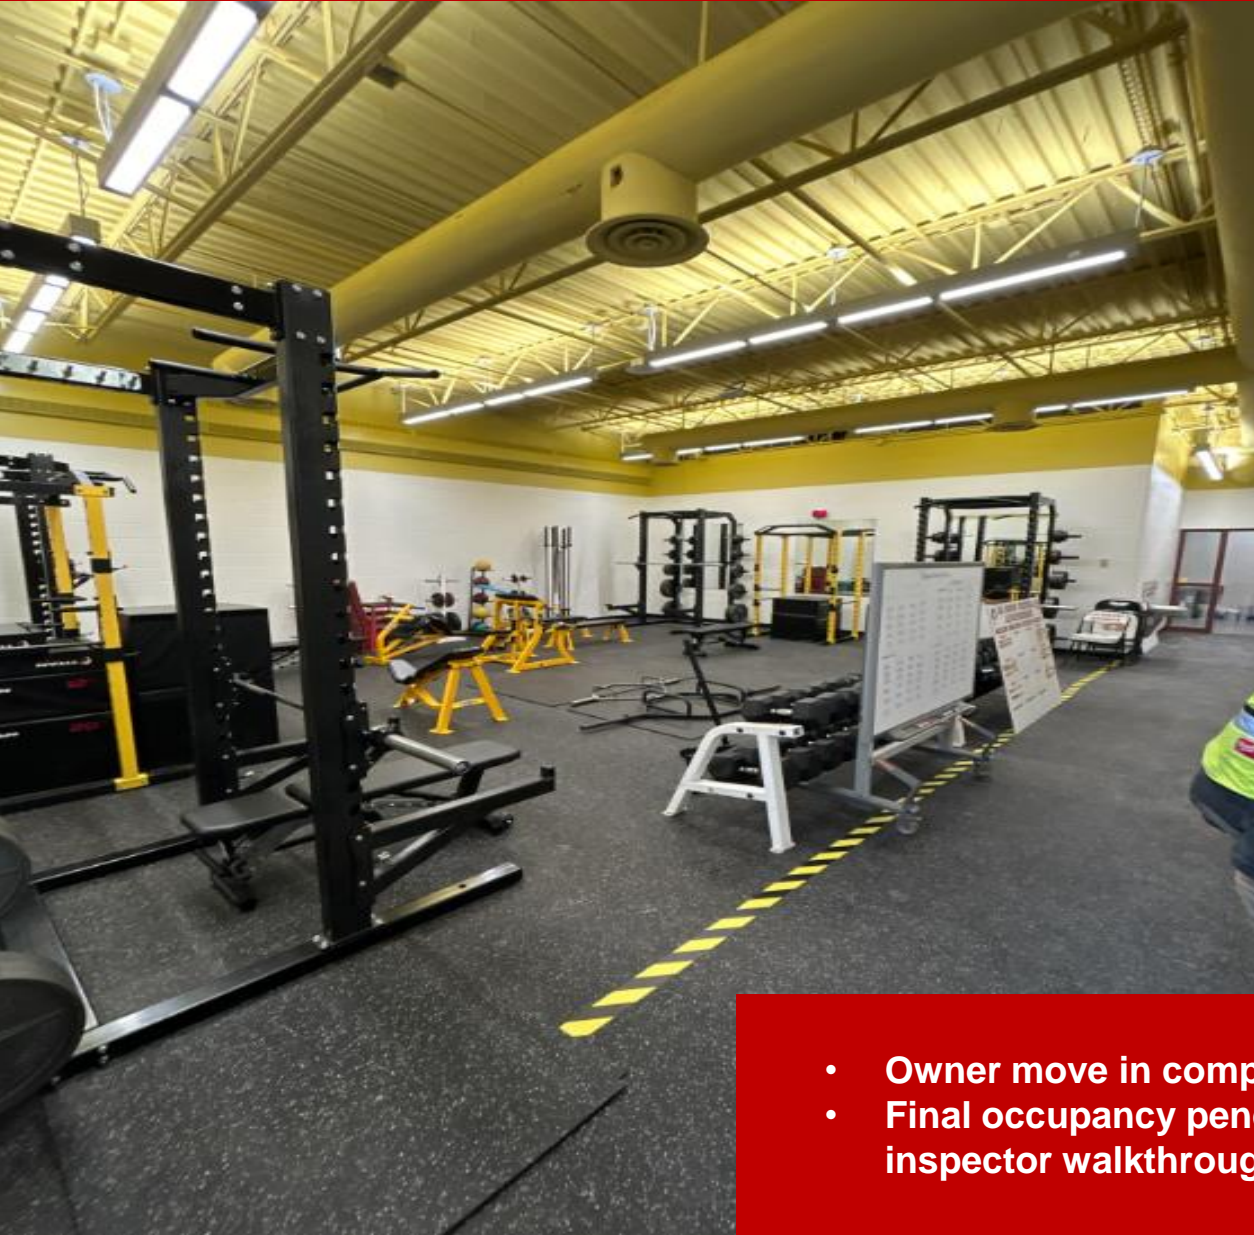

- Owner move in complete
- Final occupancy pending building inspector walkthrough.

# TWO WEEK LOOK AHEAD



## Multi-Purpose

- ▶ Finish remaining deck install.
- ▶ Deck delivery for Robotics Wednesday 1/3/23.
- ▶ Scheduling final building inspection for weight room this week.
- ▶ Continue z-girts and flashing for metal panel installation.
- ▶ Begin exterior metal framing for fascia & soffit.
- ▶ Kalwall window blocking and roof blocking on high gym roof and robotics.
- ▶ Install roof curbs and rails for mechanical units.
- ▶ Finish remaining CMU needed to complete decking.

## Weight Room

- ▶ Scheduling inspection for weight room this week
