

Presented by Construction & Facilities

# Alief ISD Bond Construction Update

Presenter Glenn Jarrett  
Director/Construction & Facilities



# Project Synthetic Turf at Auxiliary & Taylor Fields



**Architect: BRW Architects**

**Contractor: Hellas**

**Project Budget: \$4,770,000**

**Project Award: \$6,899,851**

**The \$2,129,851 is covered by bond savings from other projects.**

**Scope of Work:**

## **Elsik High School Track and Turf Replacement**

- Replace track to include demolition, grading, site/soil prep., new curbs, track foundation, track surface, striping, etc. as needed to meet UIL requirements.
- New synthetic turf field with drainage system inside the new track to include new goal posts with pads, field markings, etc.

## **Annex Track Replacement**

- Replace annex track to include demolition, grading, site/soil prep., new curbs, track foundation, track surface, striping, etc. as needed to meet UIL requirements. Existing natural grass in-field to remain (not synthetic turf).

## **Taylor High School Track and Turf Replacement**

- Replace track to include demolition, grading, site/soil prep., new curbs, track foundation, track surface, striping, etc. as needed to meet UIL requirements.
- New synthetic turf field with drainage system inside the new track to include new goal posts with pads, field markings, etc.



Final surfacing complete



## Annex Track

Picture of completed tracks.





### Taylor Synthetic Turf

Picture of new synthetic turf and track.





## Elsik Synthetic Turf

Picture of new synthetic turf and track.

# Tennis Court Replacements

## Project Status

Engineer Dally + Associates, Inc.

Architect BRW

Project Status: Demo:

1 foreman, 1 operator & 2 flaggers.

Anchor Fence Delivered equipment & material. Pulled out spoils for posts in courts 9 & 10, concrete to be poured the next day for posts Miranda Trucking poured the beat wall footer, adding chairs in the process & capping exposed rebar for protection.

Pouring back concrete into the existing posts @ courts 1, 2, 5, 8, 11 & 12.



# Tennis Court Replacements



Tennis Court  
Picture of new practice wall.

# District Wide Secure Entries - Video Intercom

Project Status



Project Design: In-house Construction Department

Project Budget \$ 1,200,000

Contract Award: \$363,873

Bond Savings: \$836,127

ASAP was awarded the Video Door Bell Projects

This consist of installing a video door bell device at each entrance to every building in the district

Currently ASAP has installed 38 of 49 locations.

# Crump Stadium Press box Improvements



Project Status

NON Bond Project

Project Design: PBK Sports

Project Budget from 2015 Bond Savings: 6,000,000

Contract Award: TBD

Project Scope: Provide ADA access to the press box along with improvements to the interior

SUPERINTENDENT PROJECT ADVISORY TEAM (PAT) meeting #3 Scheduled for December 18<sup>th</sup>



# Agricultural Science Center Project



## Project Status

Project Design: Stantec Architects

Project Budget 12,000,000


Contract Award: Bartlett Cocke CMAR

Project Scope: Design and Deliver a New Agricultural Science Center

Completed our last PAT meeting, design team can now complete the DD Phase and make our presentation to the board in November.



# Design Progress – Site Plan

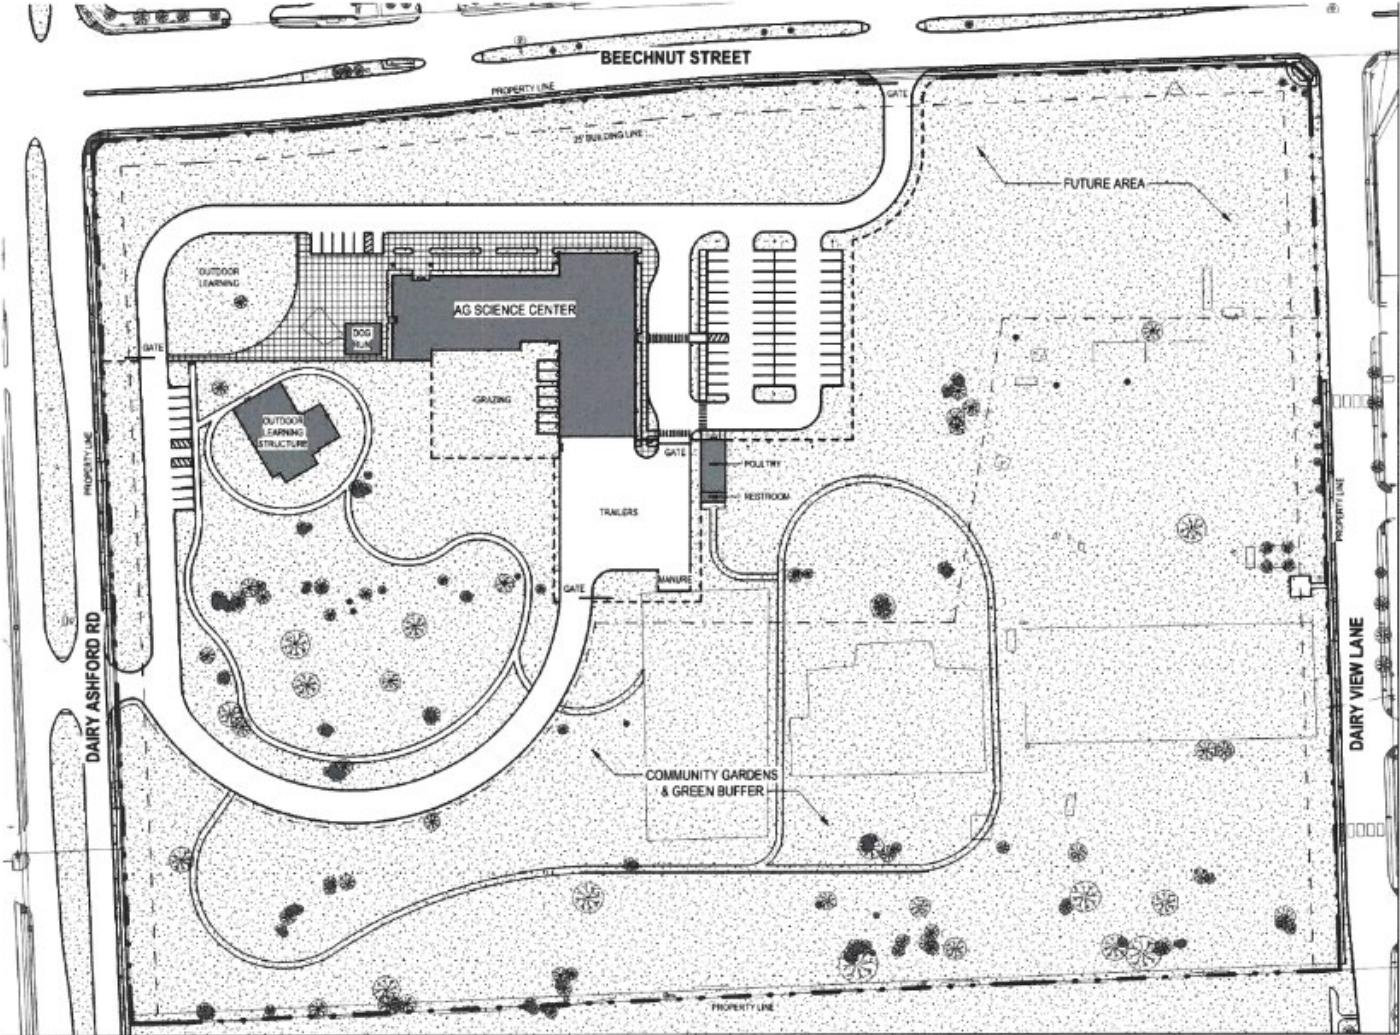

## Agricultural Science Center Proposed Site Plan
