

Presented by Construction & Facilities

Alief ISD Bond Construction Update

Presenter Glenn Jarrett
Director/Construction & Facilities



Tennis Court Replacements

Project Status

Ongoing 3/3/2025:

- Wash out dumpster delivered
- Court 3/4: Finished final grading and last fence post sleeves secure in footings; Finished vapor barrier, cables, net posts & rebar install
- Final painting completed at courts 5&6, stripping at courts 7&8
- Asphalt installed around court 9&10 and CO areas

-
Continuing work on fence improvement works as per CO for 11/12, did cut/cap at 10ft; handled the additional ties requested at Courts 9/10 -Beat wall skim coat


- Prepping of existing courts for new finishes complete.

-
J&S Requested Client to verify/mark out the locations of the bleachers/canopies on the ground next week to finalize locations so that team may start installing footers.

Upcoming:

- Court 3/4: Observations on pre-install meetings for fences gates / inspect footings-cables; POUR - targeting next Tuesday
3/11/2025 for pre-reviews and 3/13/2025 for pour

- Bleachers arrival and set; bleacher awnings begin.
- Sidewalk repairs around tennis courts (Excepting 3/4) complete.
- Paint beatwall and install metal coping cap
- Continue installing all new fencing improvements (excepting courts 3&4)

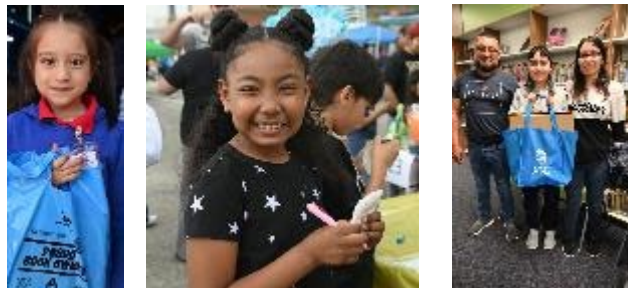

Tennis Court Replacements



Tennis Court

Picture of Court 3 & 4 cable placement and vapor barrier installed. 9 & 10 final painting of court

Tennis Court Replacements



Tennis Court
Picture of new asphalt and fencing

District Wide Secure Entries - Video Intercom

Project Status



Project Design: In-house Construction Department
Project Budget \$ 1,200,000
Contract Award: \$363,873
Bond Savings: \$836,127
ASAP was awarded the Video Door Bell Projects
Project is functionally complete working on closing project out



Crump Stadium Press box Improvements



Project Status

NON Bond Project

Project Design: PBK Sports

Project Budget from 2015 Bond Savings: 6,000,000


Contract Award: TBD

Project Scope: Provide ADA access to the press box along with improvements to the interior

Design Development was approved by the board and we are working with Purchasing getting the advertisement of CM@Risk published



Crump Stadium Press box Improvements

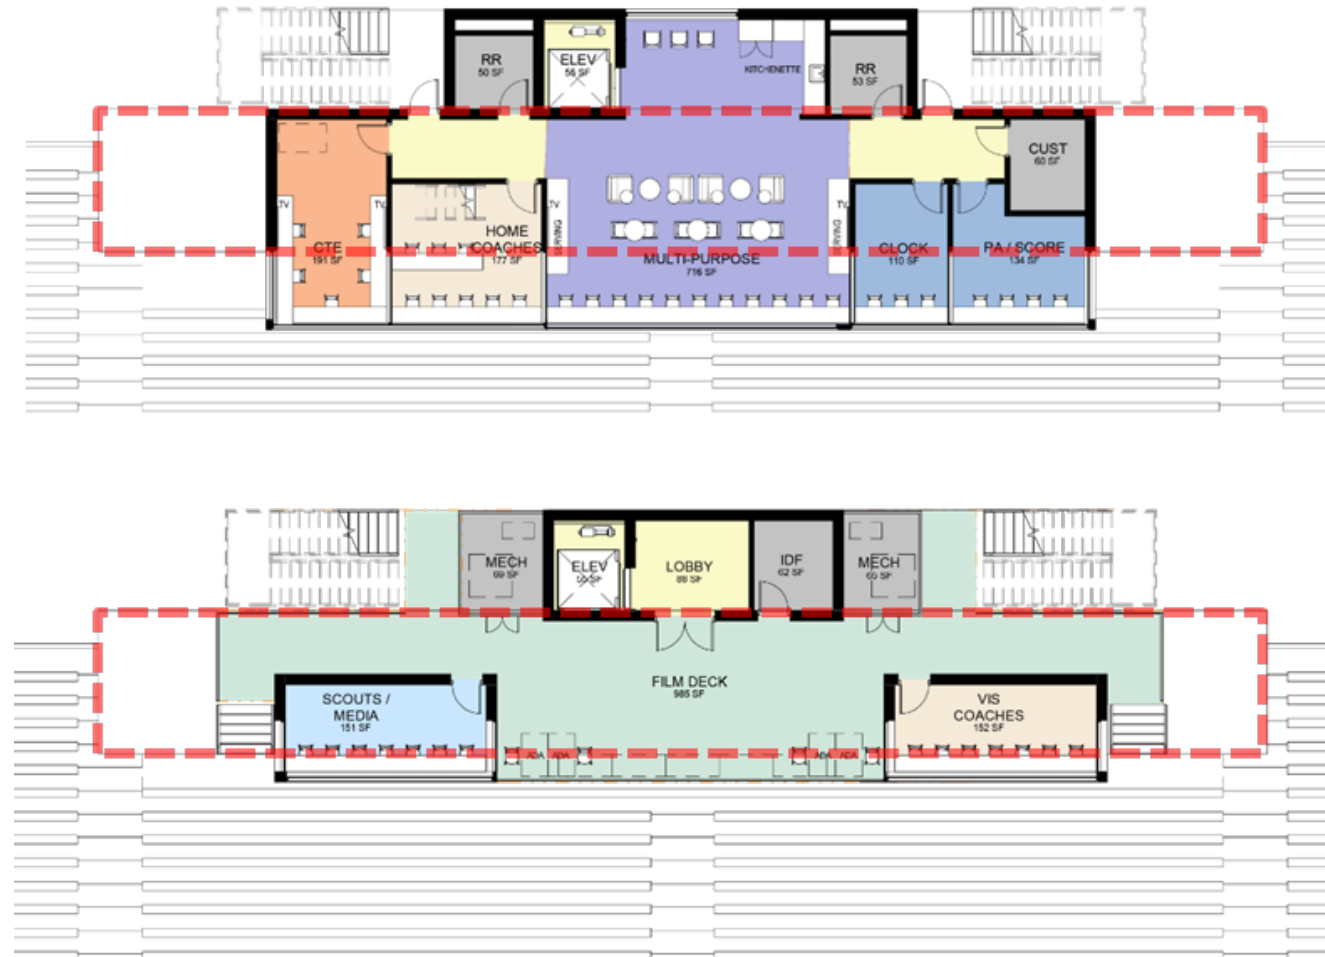

CONCEPT B

Crump Stadium Press box Improvements



OPTION B1

Agricultural Science Center Project



Project Status

Project Design: Stantec Architects

Project Budget 12,000,000


Contract Award: Bartlett Cocke CMAR

Project Scope: Design and Deliver a New Agricultural Science Center

Stantec Architects have completed the Design Development plans and have issued to Bartlett Cocke for pricing we have a review meeting scheduled for March 4th.



Design Progress – Site Plan

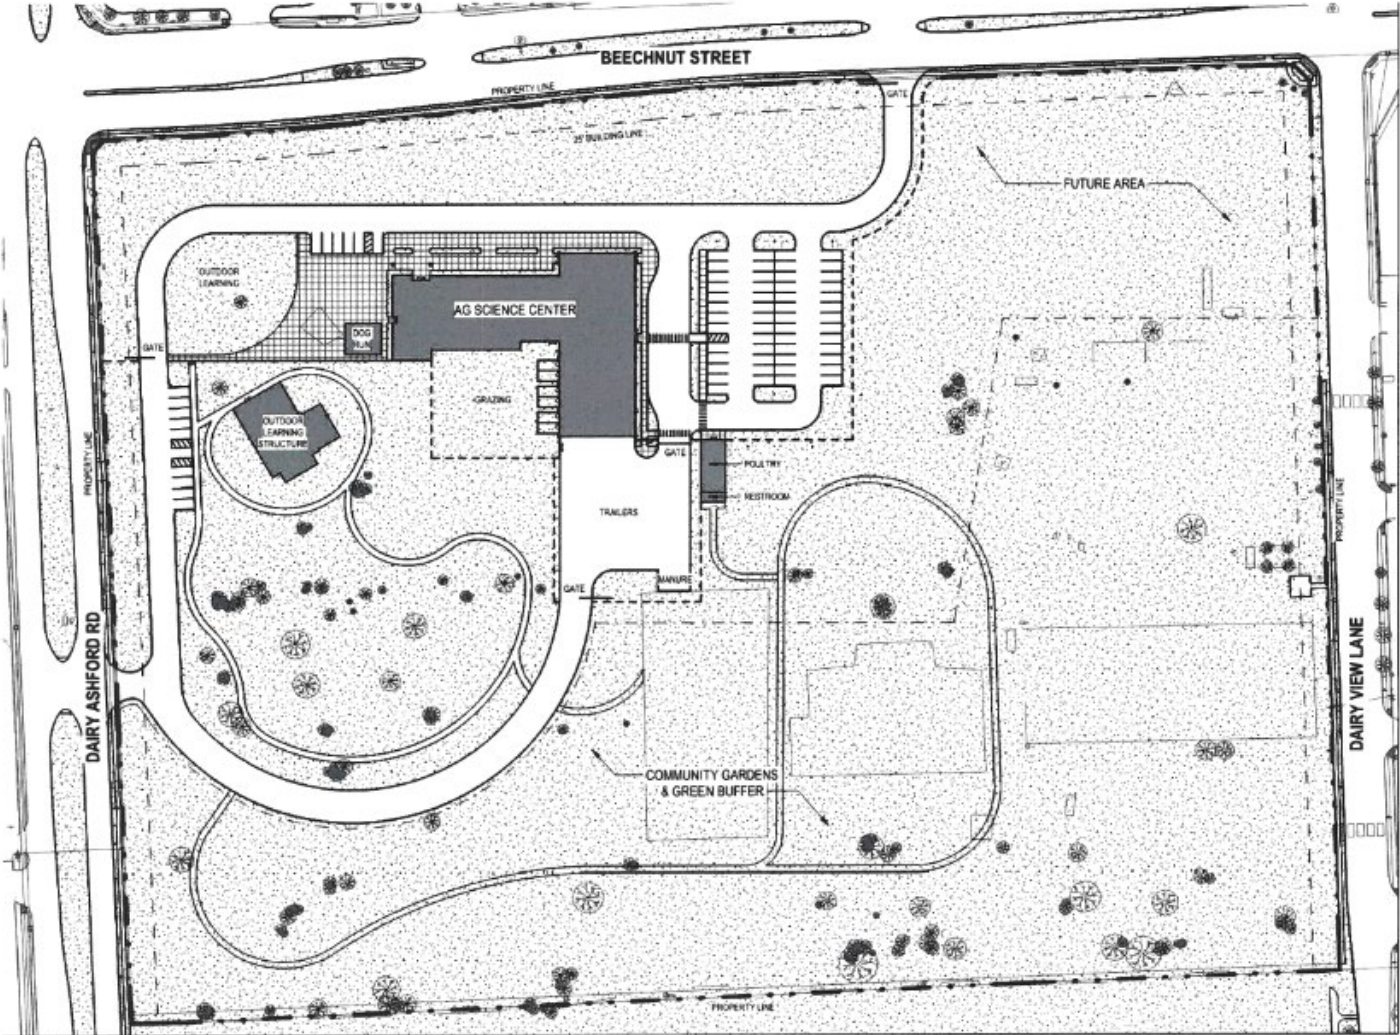

Agricultural Science Center

Proposed Site Plan



Independent School District
THE SMART CHOICE
