



# MSAD 49 Building Committee

March 2024



# Meeting Agenda

- Work Updates
- Project Schedule
- Construction Progress
- Playground Equipment
- Project Budget
- New Business

# 01.

WORK  
UPDATES


# Work Update

- Construction testing agency hired – *SW Cole Engineering*
- Clerk of the Works hired – *Jim Saucier*
- Foundations and structural steel pre-installation meeting held
- MDOT permit approved

# 02.

PROJECT  
SCHEDULE



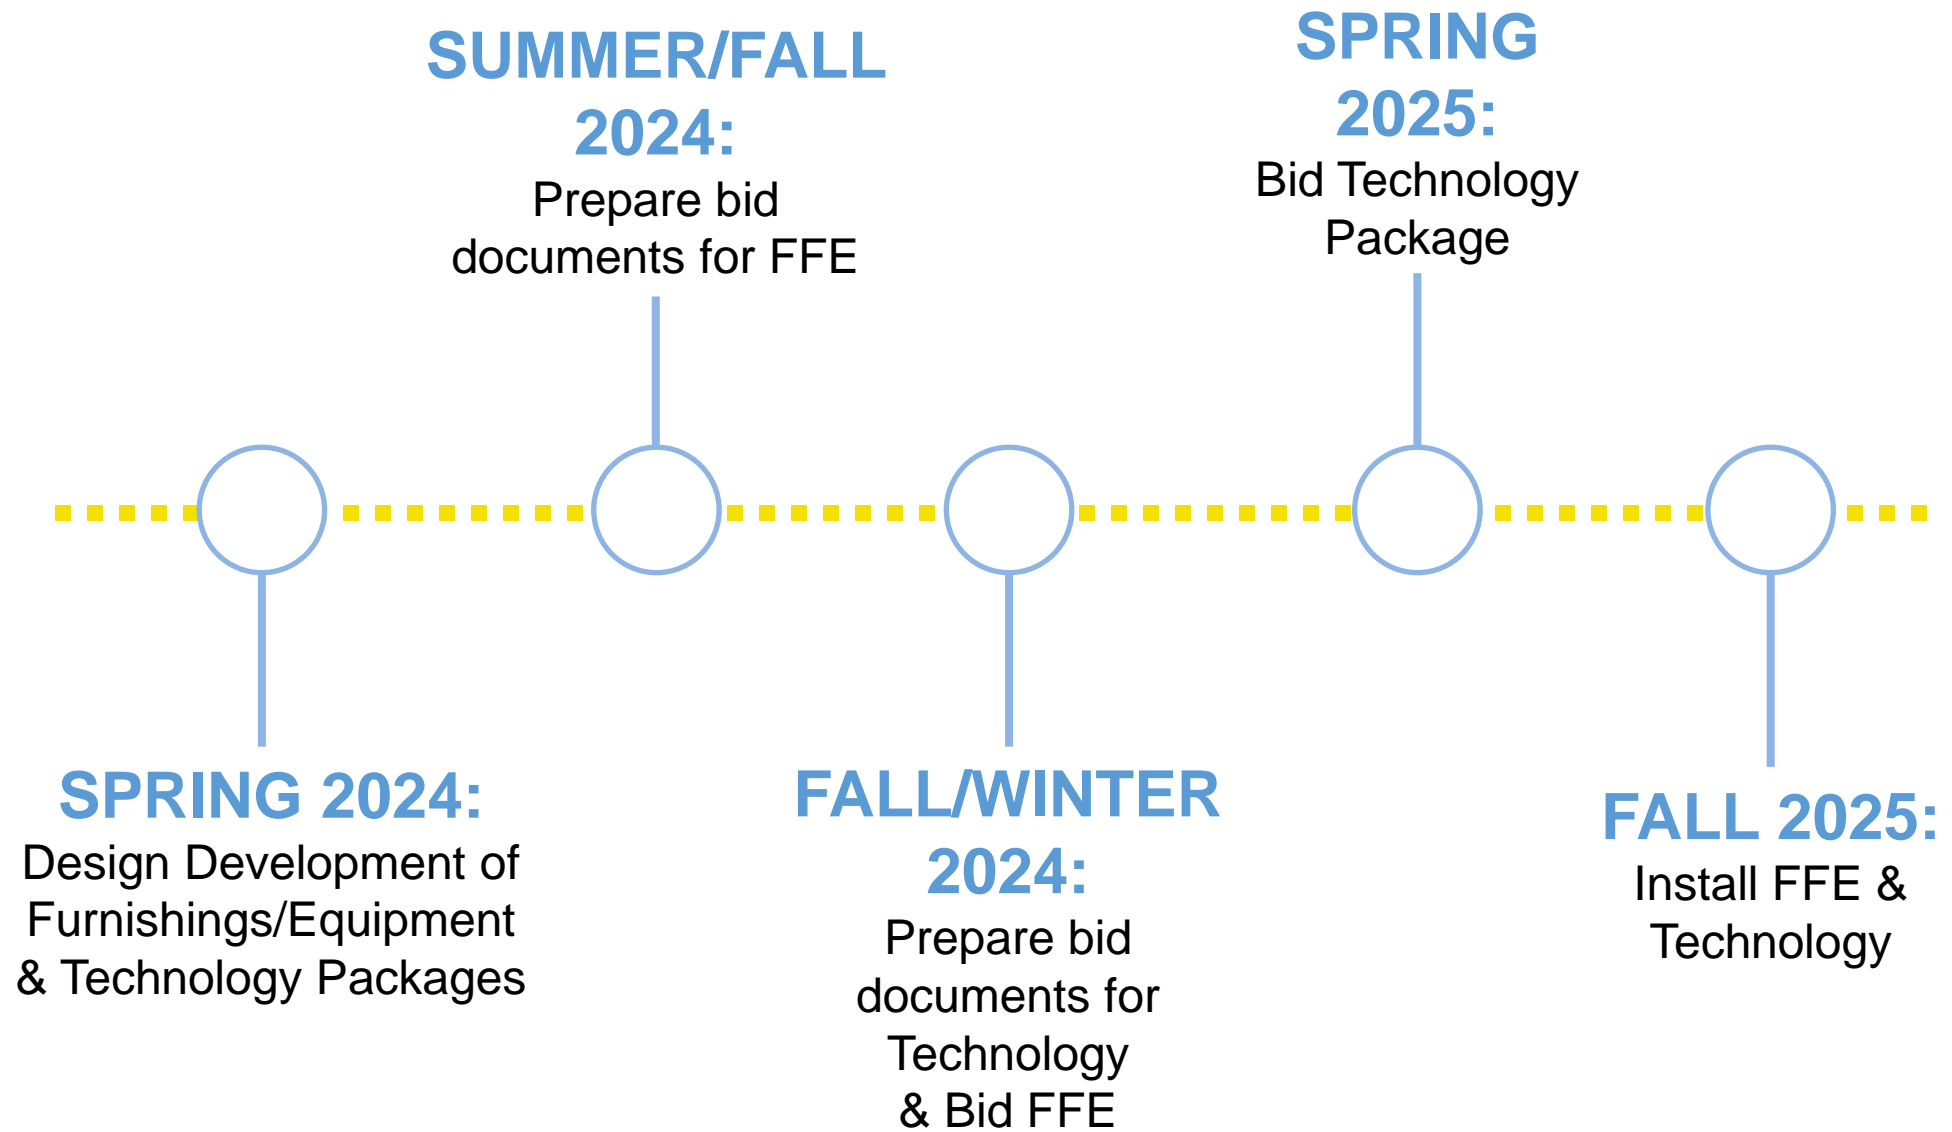

03. ■

CONSTRUCTION  
PROGRESS



# Construction Progress



Precast drainage structures



Soil filters and discharge pipes



# Construction Progress



Fill and compaction of access roads





# Construction Progress



Drilling ledge






# Construction Progress



Trenches and formwork for foundations

# Schedule & Upcoming Activities

- March
  - Site earthwork
  - Underground plumbing
  - Foundations (Area C)
- April
  - Site earthwork
  - Underground electrical
  - Foundations (Area B)
  - CMU stairwells and elevator

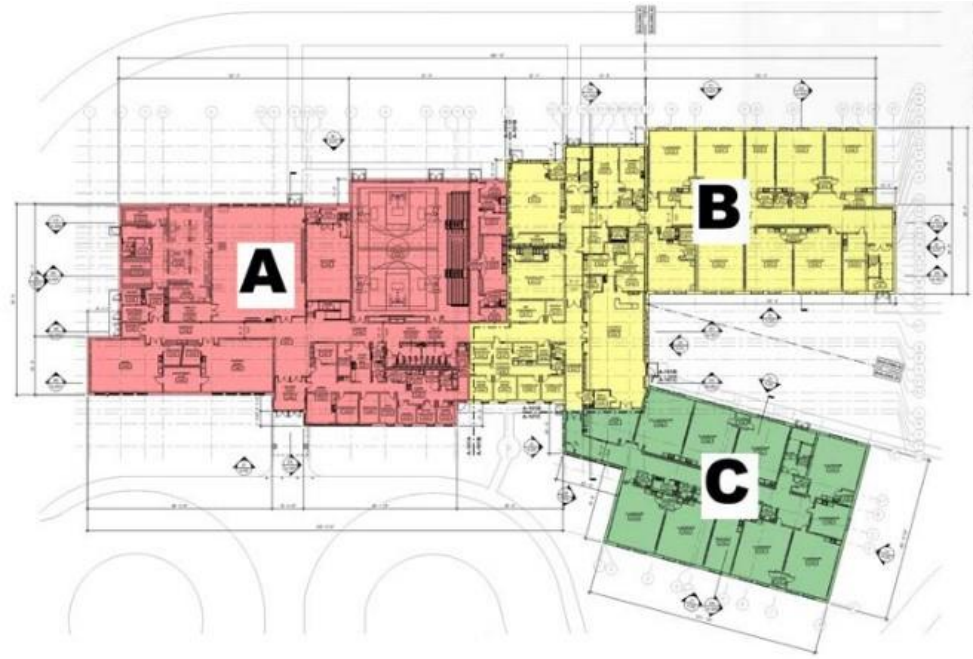


04.

PLAYGROUNDS



# New Equipment

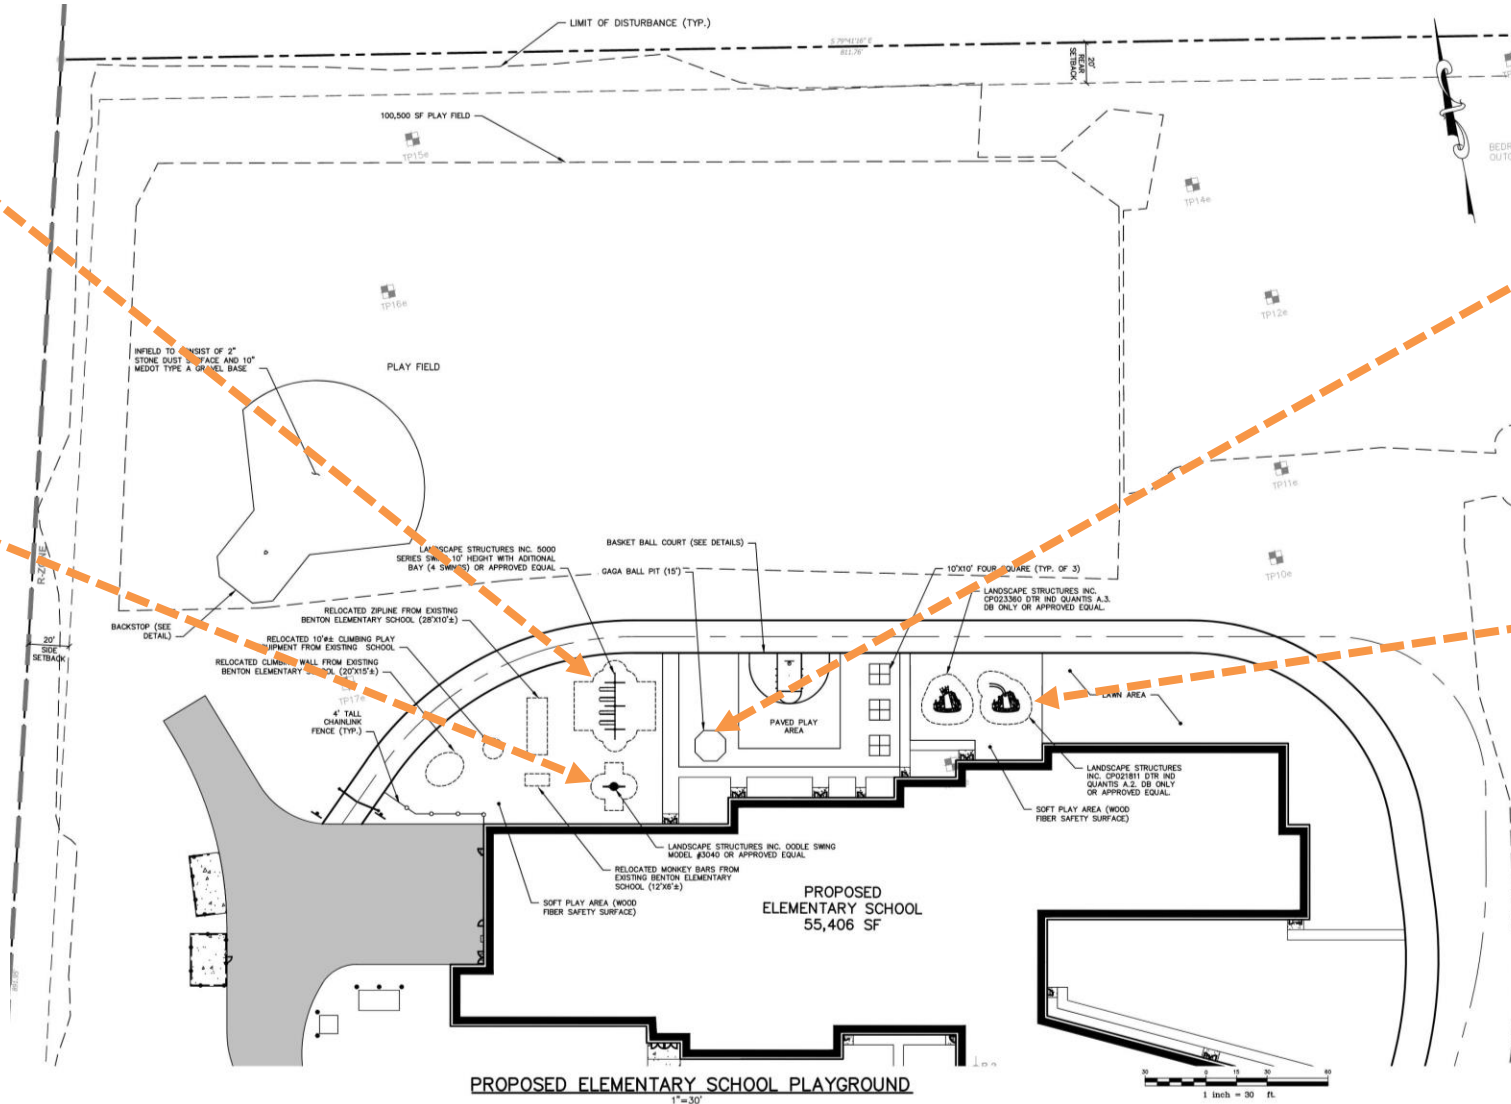

05.

PROJECT  
BUDGET



# Project Budget Update

- February Requisition: \$307,436.00,
  - 0.89% complete by contract value
- Construction Contingency: \$1,752,161.70
  - 0% expended

06. ■

NEW  
BUSINESS
