

**2021 BOND PROGRAM
CONSTRUCTION UPDATE**

**GALESBURG-AUGUSTA COMMUNITY SCHOOLS
HIGH SCHOOL MULTI-PURPOSE ADDITION &
WEIGHTROOM**

2/23/2024




MULTI-PURPOSE OVERVIEW



Construction Phasing & Site Plan High School Multi-Purpose Addition

TowerPinkster
Architecture - Engineering - Interiors

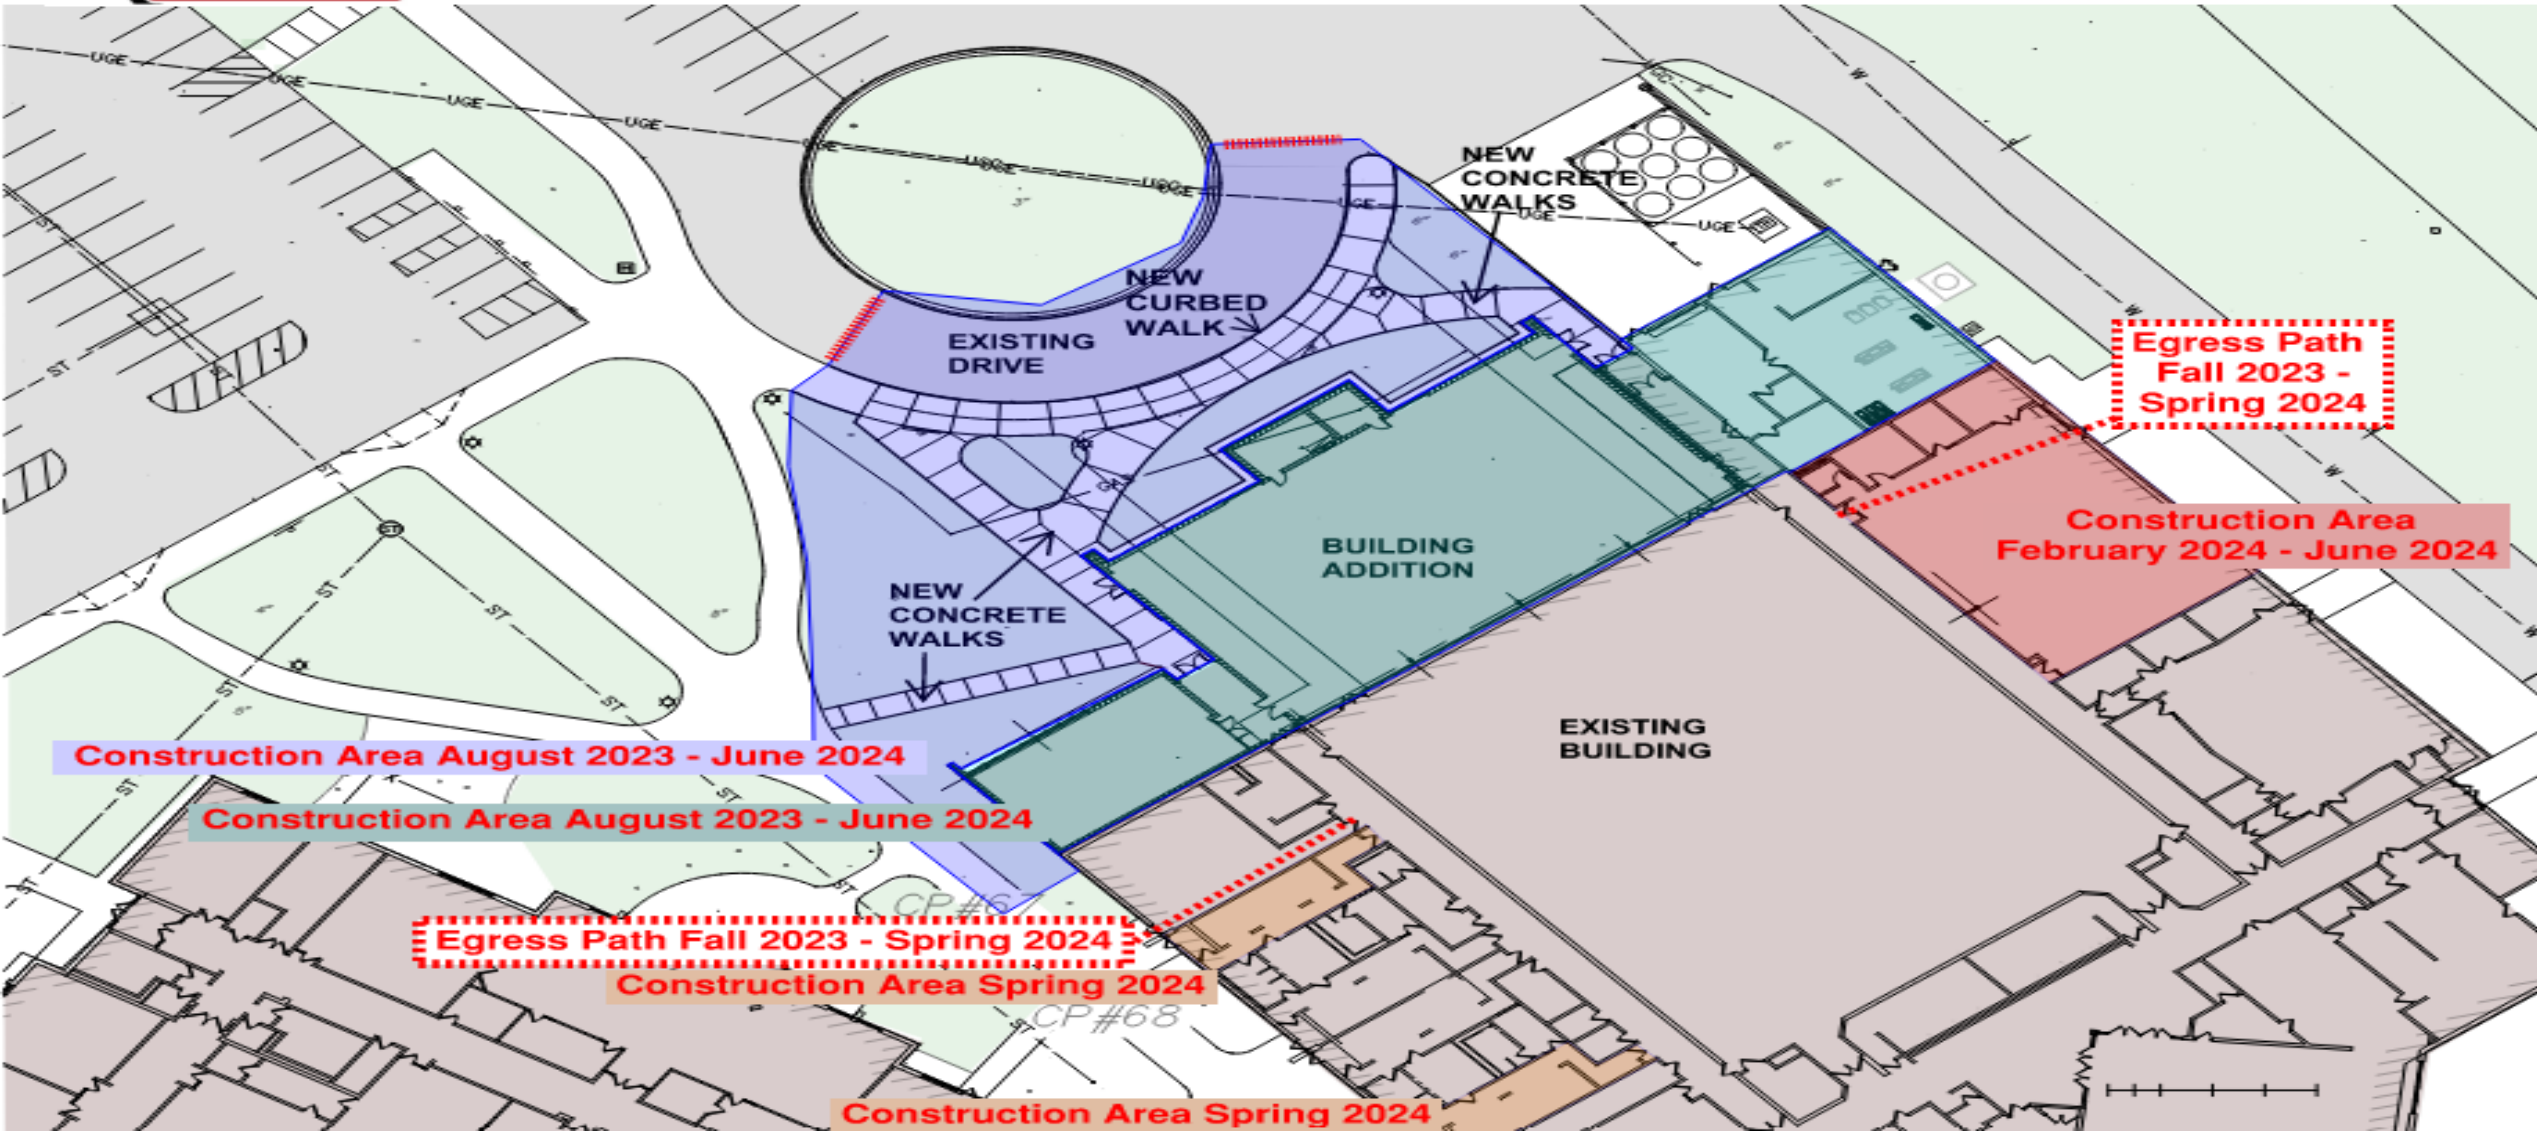


MULTI-PURPOSE OVERVIEW



- All floors have been poured
- Construction to begin spray foam next week





ROBOTICS ROOM OVERVIEW

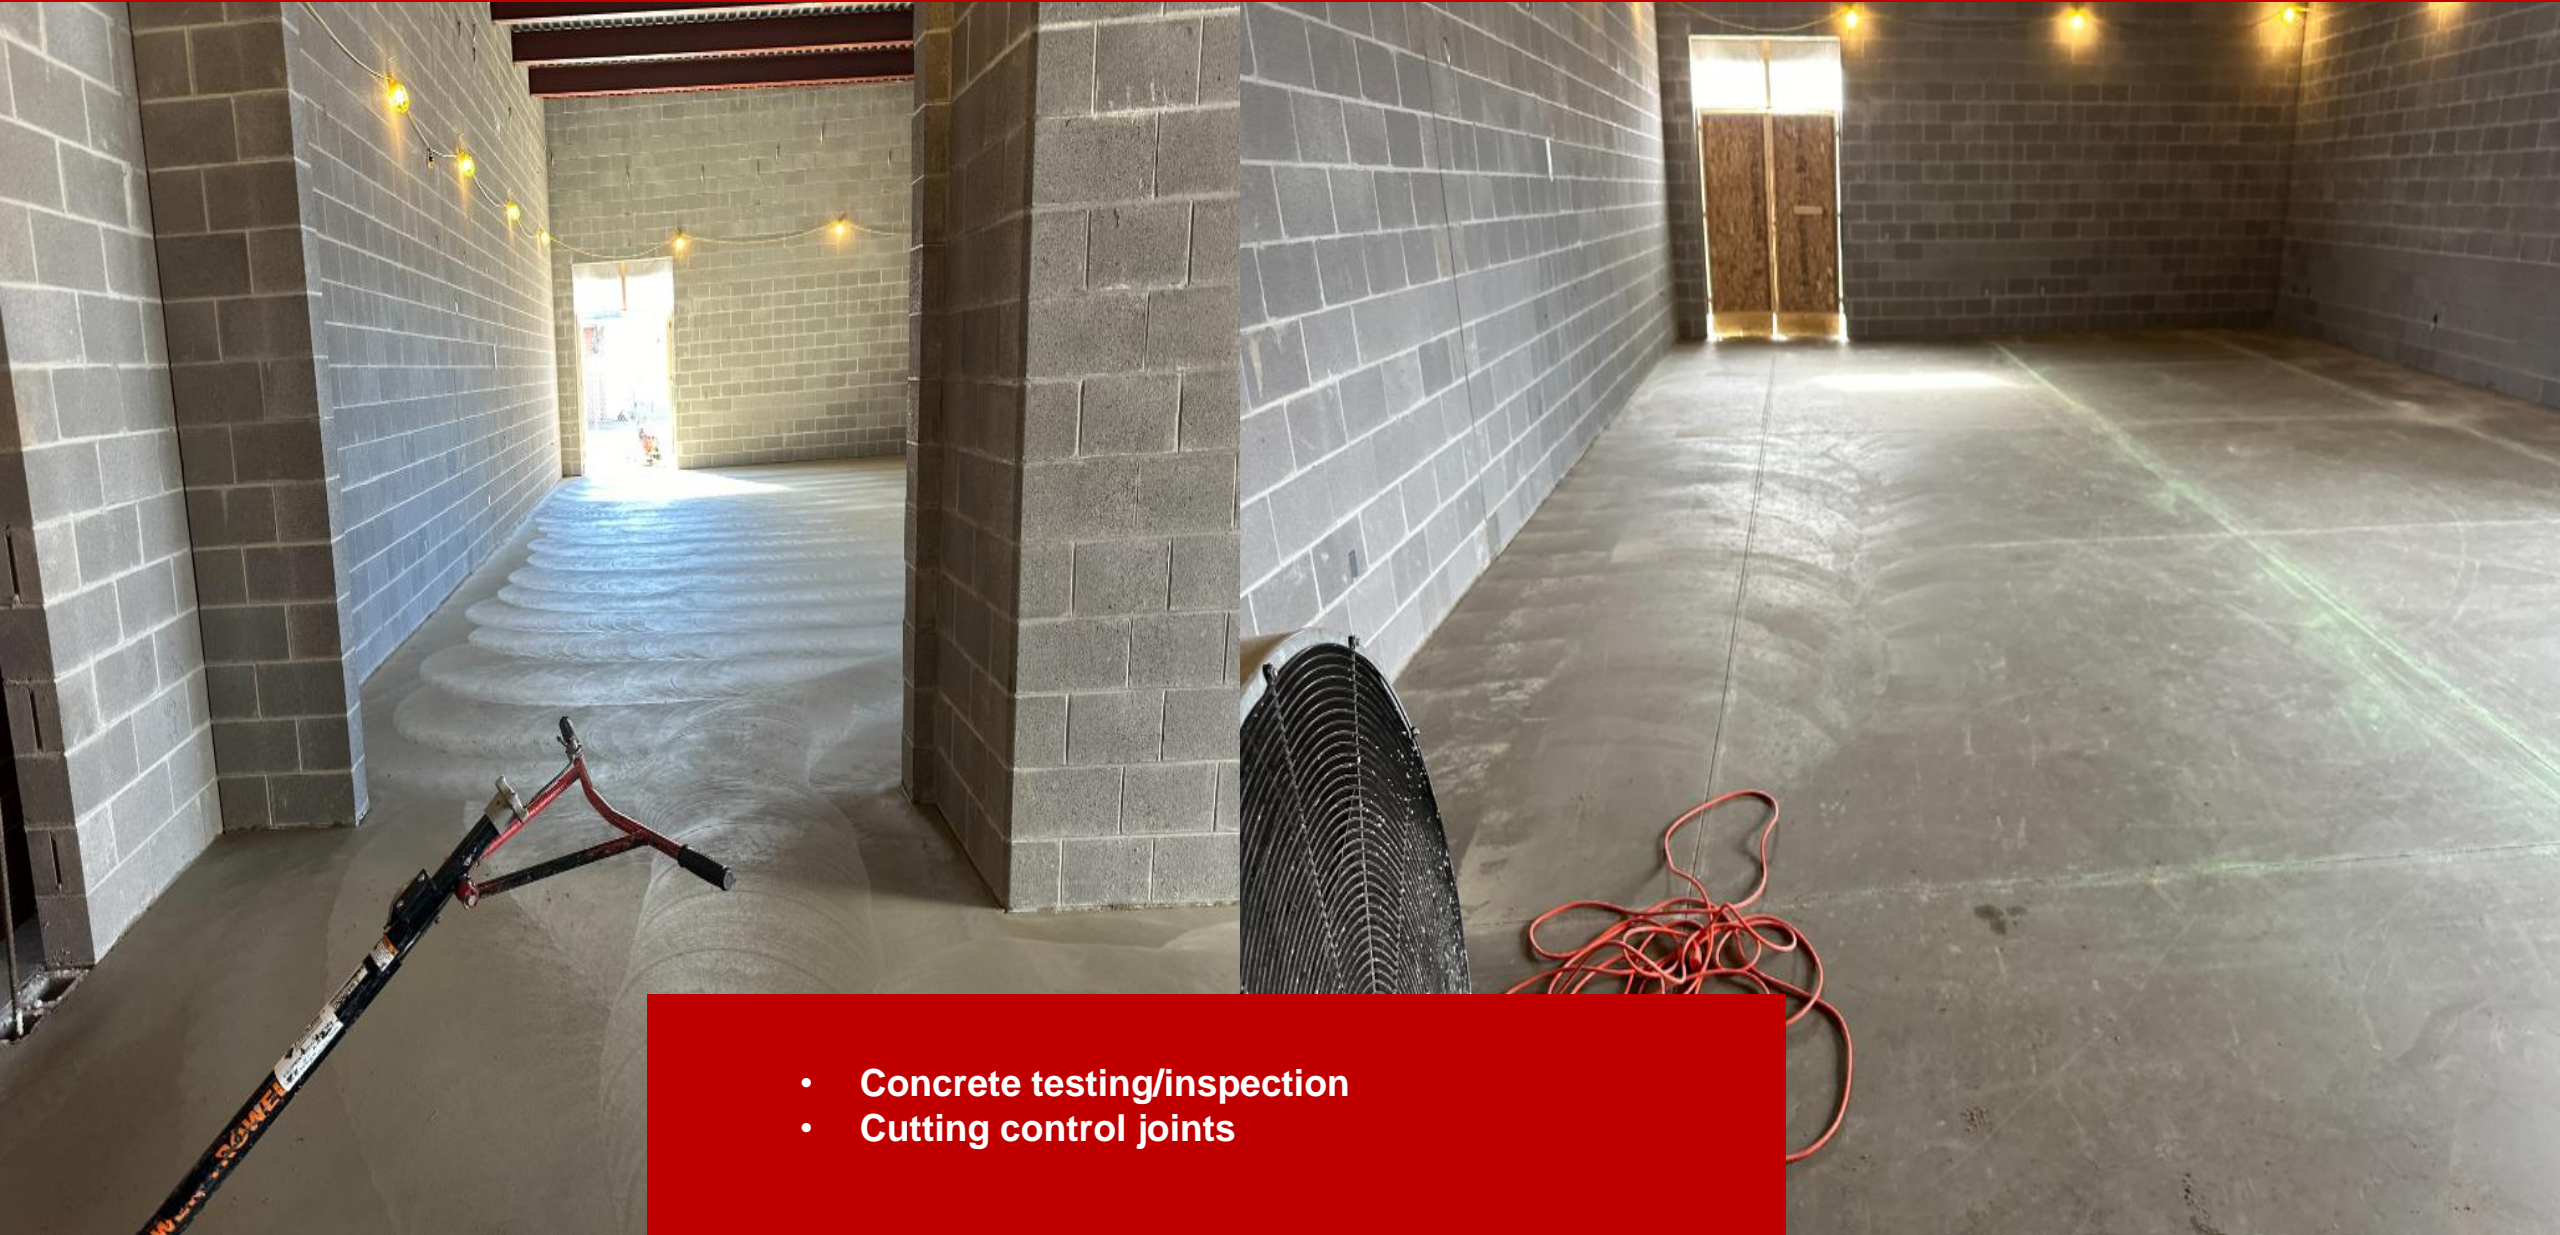

- Concrete testing/inspection
- Cutting control joints

MULTI-PURPOSE OVERVIEW

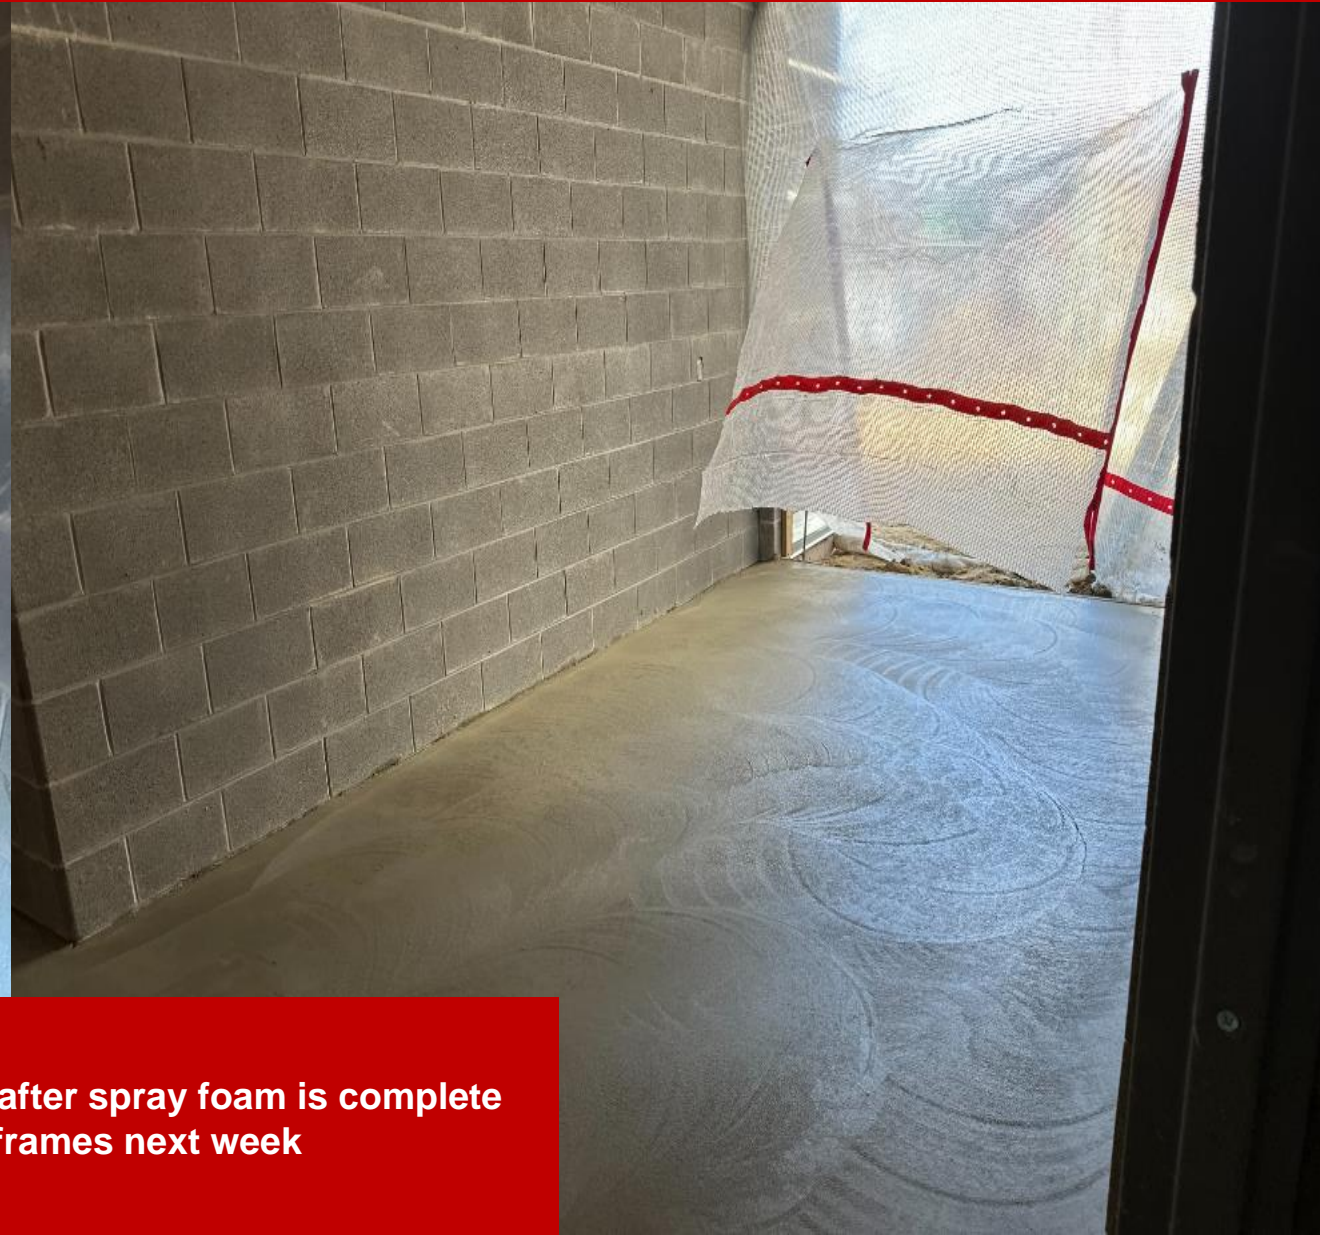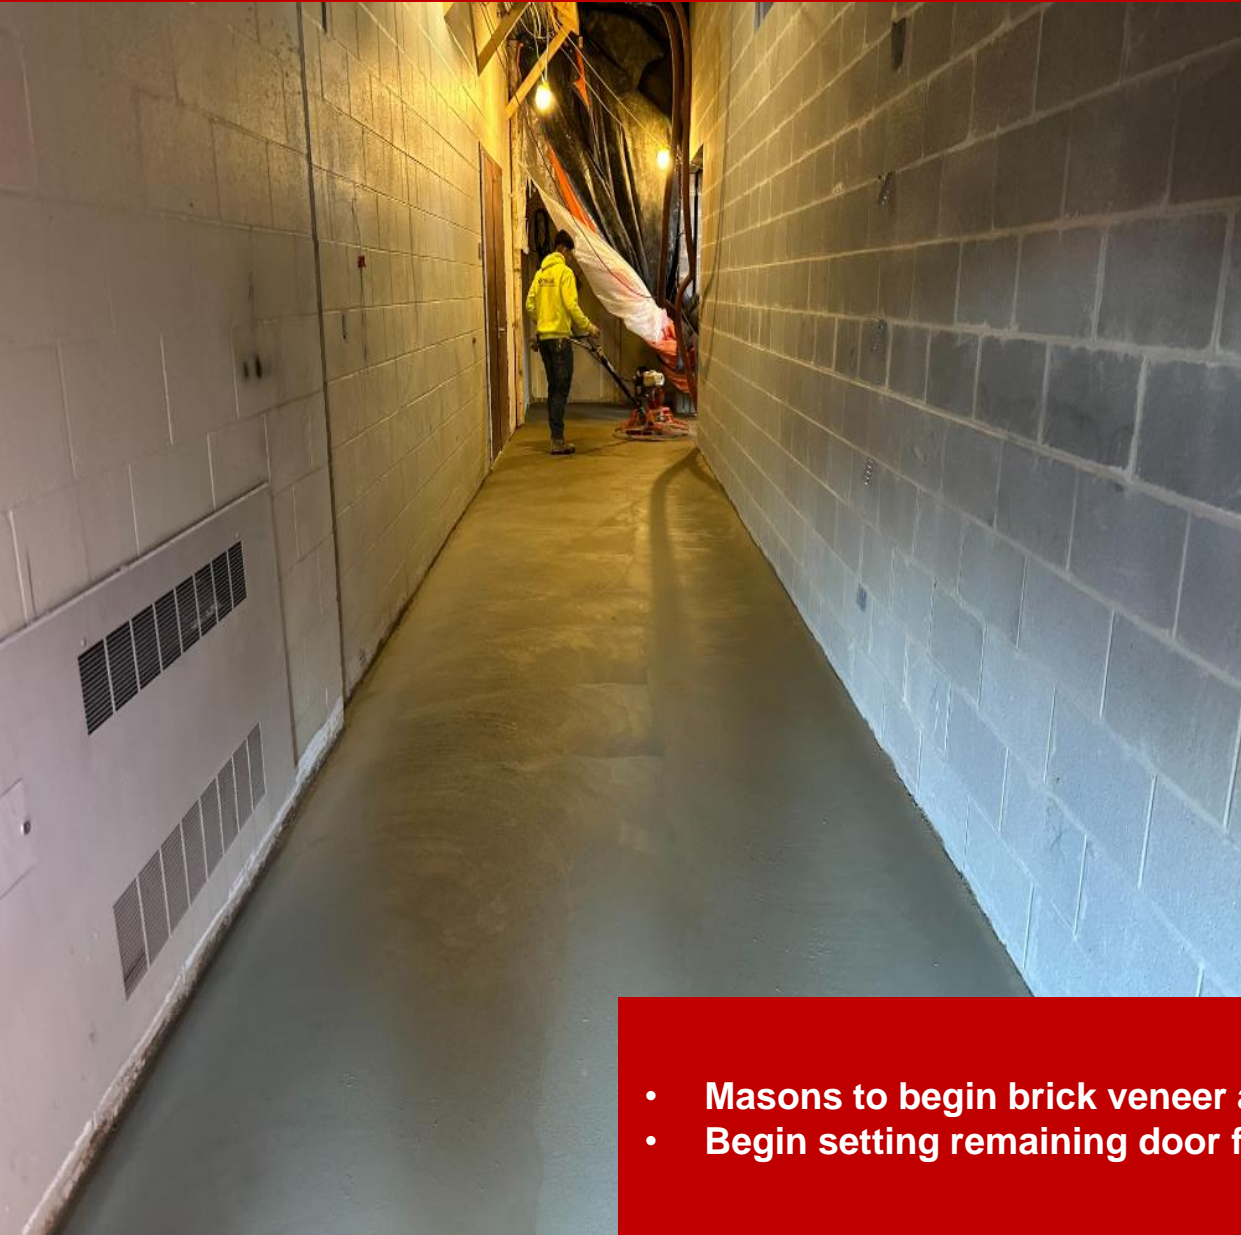

- Masons to begin brick veneer after spray foam is complete
- Begin setting remaining door frames next week

TWO WEEK LOOK AHEAD



- ▶ Electrical /Mechanical/Plumbing Overhead Rough-in start
- ▶ Setting remaining interior door frames
- ▶ Masons to begin brick veneer
- ▶ Fire protection rough-in to begin
- ▶ Structural Steel and deck for storage room to be completed
- ▶ Portal door frame/masonry openings to begin
- ▶ Begin spray foam insulation
