



Schenectady

City School District

Board of Education Update

November 15, 2023

Facilities RoadMap



ENGAGE • IMAGINE • INSPIRE

Jacobs |  LECHASE

BOE Presentation Agenda

November 15, 2023

1. Early Phase Projects
2. Additional Early Phase Projects
3. Other Project Updates
4. SCSD Revitalization Plan 2030



Schenectady City School District



#SchenectadyRising

Reopening, rebuilding and reigniting Schenectady City Schools with a commitment and dedication to ***excellence in teaching and learning, equity, engagement and efficiency.***

EVERYBODY COUNTS. EVERYBODY LEARNS.

1. Early Phase Projects

- a. Schenectady High School – Multiuse Outdoor Courts Project
- b. Mont Pleasant Middle School – Track & Field Project
- c. Paige Elementary School – Asbestos Abatement Project
- d. Washington-Irving – Domestic Waterline Replacement



INSPIRE



IMAGINE




ENGAGE



1. Early Phase Projects

a. Schenectady High School – Multiuse Outdoor Courts

Before: June 2023

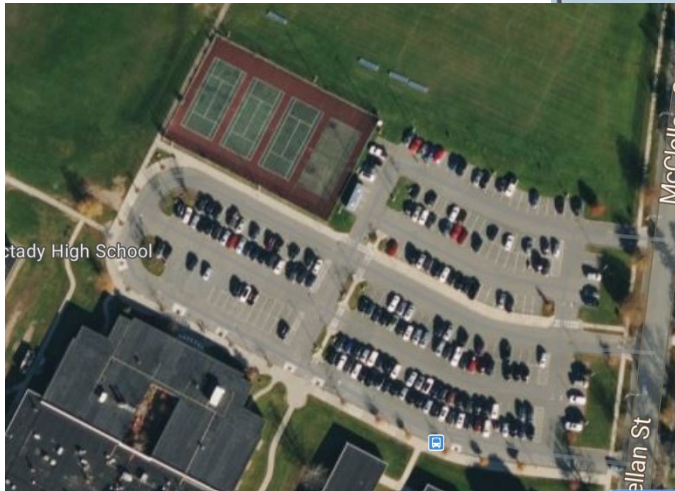



1. Early Phase Projects

a. Schenectady High School – Multiuse Outdoor Courts

Projected Completion: June 2024



1. Early Phase Projects

a. Schenectady High School – Multiuse Outdoor Courts

Projected Completion: June 2024



1. Early Phase Projects

a. Schenectady High School – Multiuse Outdoor Courts

Projected Completion: June 2024





1. Early Phase Projects

a. Schenectady High School – Multiuse Outdoor Courts


Projected Completion: June 2024



1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Before: June 2023

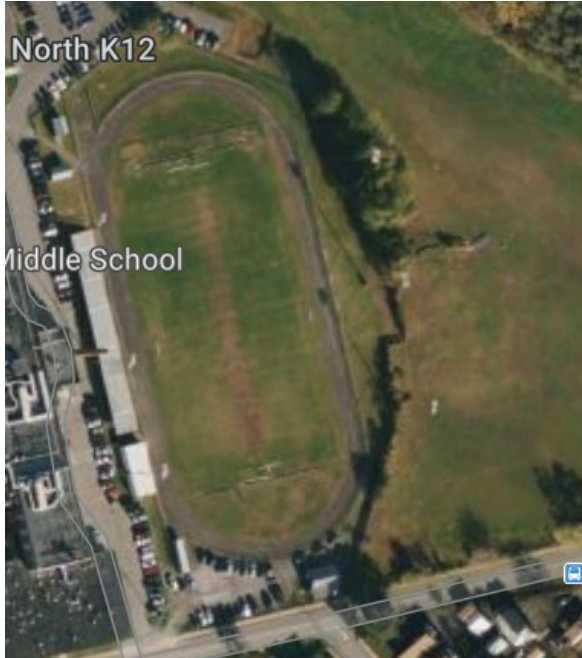

1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Groundbreaking: October 2023





1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Projected Completion: August 2024





1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Projected Completion: August 2024





1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Projected Completion: August 2024





1. Early Phase Projects

b. Mont Pleasant Middle – Track & Field Project

Projected Completion: August 2024





1. Early Phase Projects

c. Paige Elementary School – Abate Confined Space

- **Crawlspace Abatement Work:**

Completed: August 2024

- **Concrete Flowable Fill & Exterior Access Door:**

Projected Completion: April Break 2024

- **Remaining General Construction, Mechanical, Electrical Work:**

Projected to be completed as part of Capital Project (if required).



INSPIRE



IMAGINE




ENGAGE



1. Early Phase Projects

c. Paige Elementary School – Abate Confined Space

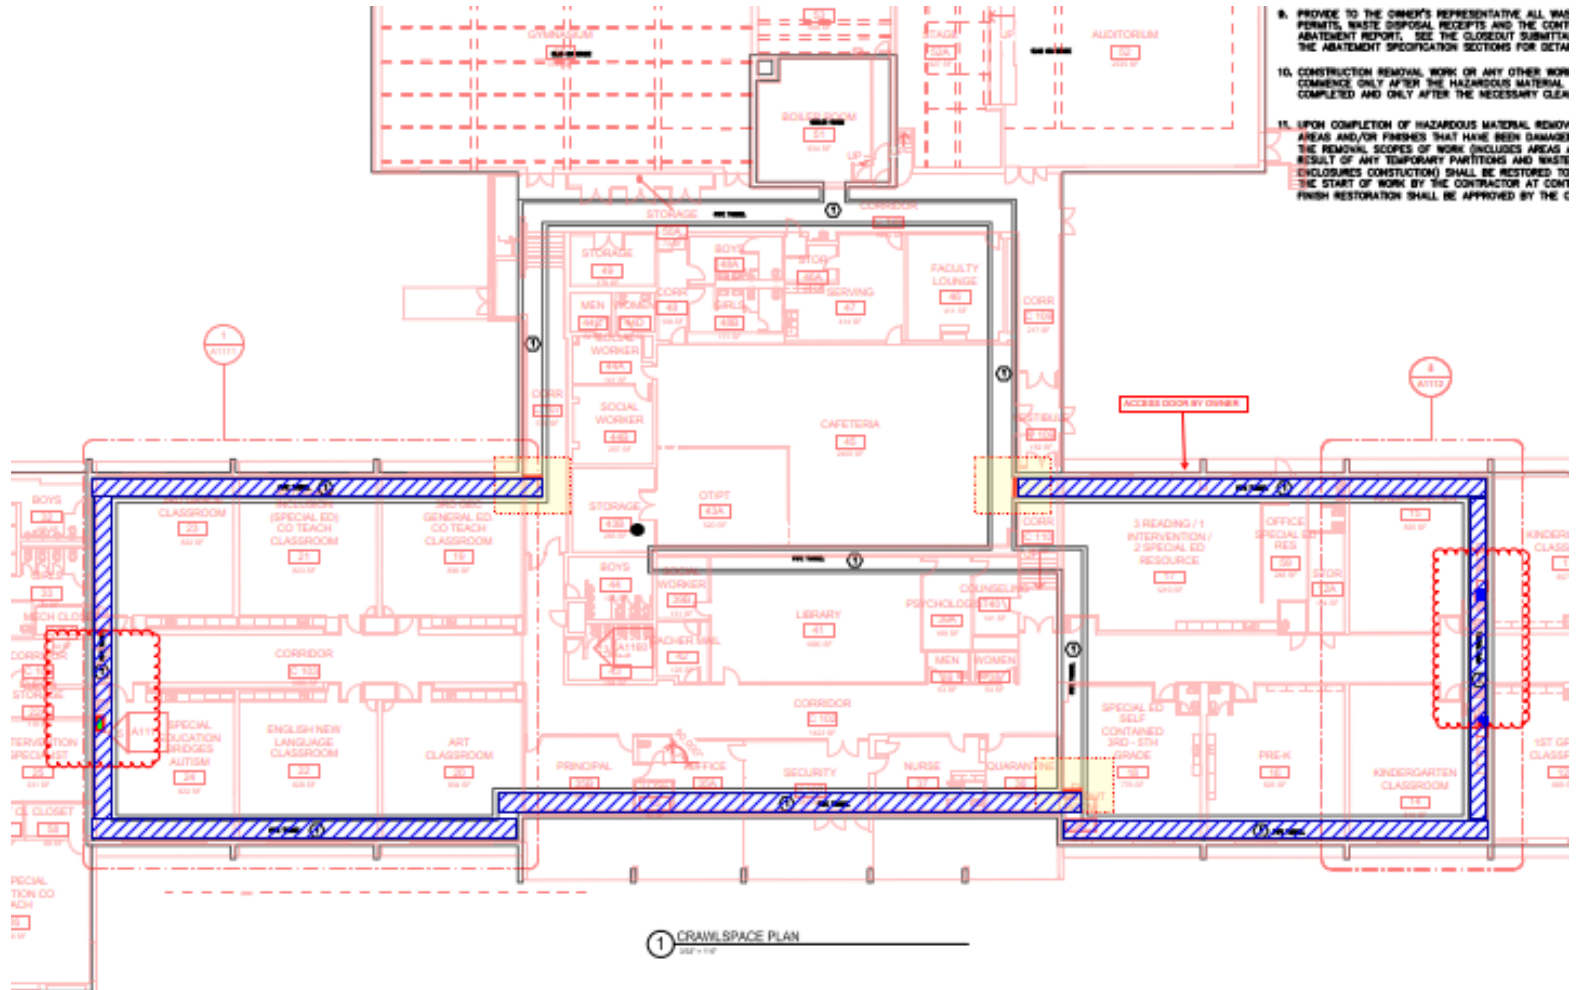

- 9. PROVIDE TO THE OWNER'S REPRESENTATIVE ALL WAS PERMITS, WASTE DISPOSAL RECEIPTS AND THE COM ABATEMENT REPORT. SEE THE CLOSEDOUT SUBMITTA THE ABATEMENT SPECIFICATION SECTIONS FOR DETAI
- 10. CONSTRUCTION REMOVAL WORK OR ANY OTHER NON COMMENCE ONLY AFTER THE HAZARDOUS MATERIAL COMPLETED AND ONLY AFTER THE NECESSARY CLEA
- 11. UPON COMPLETION OF HAZARDOUS MATERIAL REMOY AREAS AND/OR FINISHES THAT HAVE BEEN DAMAGE THE REMOVAL SCOPES OF WORK (INCLUDES AREAS I RESULT OF ANY TEMPORARY PARTITIONS AND WASTE ENCLOSURES CONSTRUCTION) SHALL BE RESTORED TO THE START OF WORK BY THE CONTRACTOR AT COMI FINISH RESTORATION SHALL BE APPROVED BY THE C





1. Early Phase Projects

c. Paige Elementary School – Abate Confined Space



2. Additional Early Phase Projects

a. **Hamilton Elementary School – Emergency Parapet Project**

Part 1: Parapet & Pre-Cast Cap Replacement – Completed: SEPT 2023.

Part 2: Parapet, Pre-Cast Cap & Roof Replacement – Completed: OCT 2023.

Part 3: Front Parapet, Cap Repair & Replacement – Completed: NOV 2023.

b. **Mont Pleasant Middle School – Emergency Sewer Line Replacement**

Completed: OCTOBER 15, 2023.

c. **Mont Pleasant Middle School – Concession Building**


Status pending, with possible construction completion by DEC 2024.



2. Additional Early Phase Projects

a. Hamilton School – Emergency Parapet Project

Part 1: Parapet & Pre-Cast Cap Replacement – Completed: SEPT 2023.

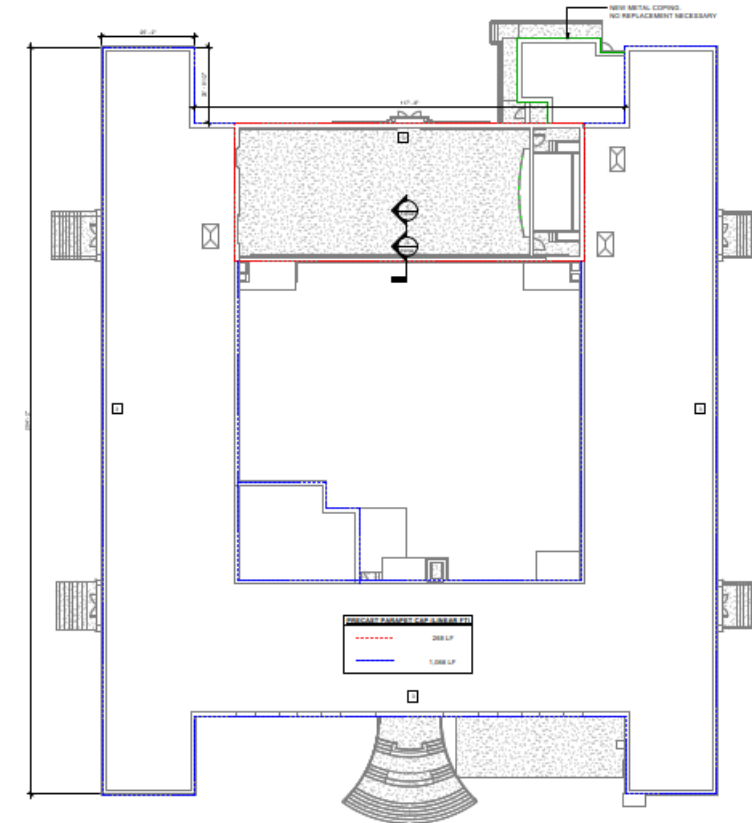

2 OVERALL ROOF PLAN





2. Additional Early Phase Projects

a. Hamilton School – Emergency Parapet Project

Part 1: Parapet & Pre-Cast Cap Replacement – Completed: SEPT 2023.





2. Additional Early Phase Projects

a. Hamilton School – Emergency Parapet Project

Part 1: Parapet & Pre-Cast Cap Replacement – Completed: SEPT 2023.





INSPIRE



IMAGINE



ENGAGE



2. Additional Early Phase Projects

a. Hamilton School – Emergency Parapet Project

Part 2: Parapet, Pre-Cast Cap & Roof Replacement – Completed: OCT 2023.

Part 3: Front Parapet, Cap Repair & Replacement – Completed: NOV 2023.






2. Additional Early Phase Projects

a. MPMS – Emergency Sewer Line Replacement

Completed: OCTOBER 15, 2023.

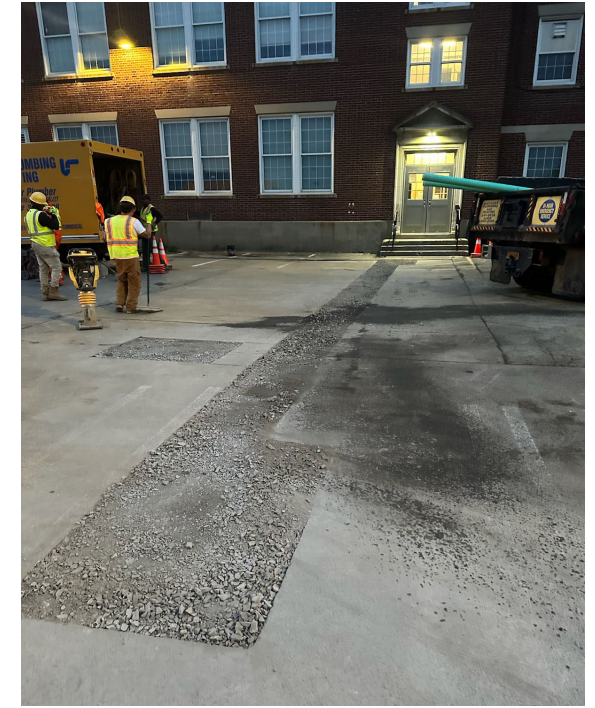



2. Additional Early Phase Projects

a. MPMS – Concession Building

Status pending, with possible construction completion by DEC 2024.



3. Other Project Updates

- a. District Wide Security**
- b. Playgrounds**
 - Hamilton
 - Woodlawn
 - Martin Luther King
 - Pleasant Valley
- c. District Office Relocation**



3. Other Project Updates

a. District-Wide Security

Day Automation has been engaged with the Schenectady City School District since 2021 with the goal of updating and improving district-wide security technology standards. The goal of the projects has been to bring all buildings up to a standard level of security that meets current best practices. This work includes:

1. Lockdown systems that automatically alert first responders of a building in lockdown
2. Creating a secure building perimeter to control access to buildings and know if any doors are propped open
3. Upgrading and expanding building intrusion systems
4. Upgrading and expanding coverage of video surveillance systems
5. Providing new PA systems at each building to include audio and visual communication capabilities

| Building | Standardized Building Lockdown | Automatic 9-1-1 Notification of Lockdown | Secure Perimeter | New Intrusion | Camera Coverage Upgrades | New PA System |
|-----------------------|--------------------------------|--|------------------|---------------|--------------------------|---------------|
| Schenectady HS | Complete | Complete | Complete | Complete | Complete | To Be Done |
| Mont Pleasant MS | Complete | Complete | In Progress | In Progress | Complete | To Be Done |
| Oneida MS | Complete | Complete | In Progress | In Progress | Complete | To Be Done |
| Central Park MS | Complete | Complete | In Progress | In Progress | Complete | To Be Done |
| Steinmetz (SCLA) | Complete | Complete | To Be Done | To Be Done | Complete | To Be Done |
| Fulton ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Hamilton ES | Complete | Complete | To Be Done | Complete | Complete | To Be Done |
| Howe ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Lincoln ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| MLK ES | Complete | Complete | To Be Done | Complete | Complete | To Be Done |
| Paige ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Pleasant Valley ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Van Corlear ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| W C Keane ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Woodlawn ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Yates ES | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| Zoller ES | Complete | Complete | To Be Done | Complete | To Be Done | To Be Done |
| Washington Irving | Complete | Complete | To Be Done | To Be Done | To Be Done | To Be Done |
| District Office (new) | In Progress | In Progress | In Progress | In Progress | In Progress | To Be Done |



3. Other Project Updates

b. Playgrounds

Hamilton A & B



Woodlawn



MLK




Pleasant Valley





3. Other Project Updates

c. District Office Relocation

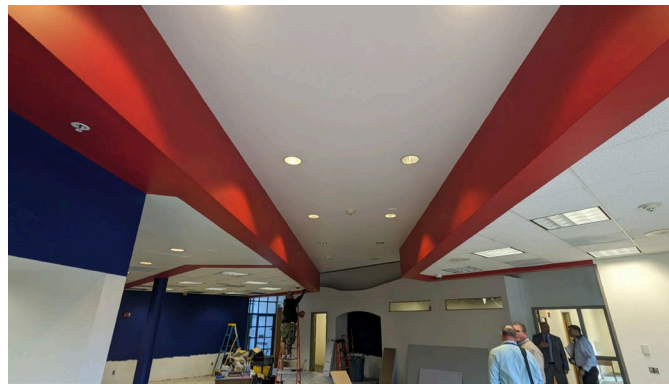

4. SCSD Revitalization Plan 2030

- a. High School Schedule Sequence Tract
- b. Elementary School Schedule Sequence Tract



INSPIRE



IMAGINE



ENGAGE



4. SCSD Revitalization Plan 2030

a. High School Schedule Sequence Tract:

beginning with 1. Steinmetz Freshman Academy...

followed by 2. SHS Core Renovations.

b. Elementary School Schedule Sequence Tract:

beginning with 1. Van Corlaer Elementary School

followed by 2. WC Keane Renovation & Addition.



4. SCSD Revitalization Plan 2030

a. High School Schedule Sequence Tract

1. Freshman Leadership Academy @ Steinmetz

| | |
|---|---------------|
| JACOBS Schematic Design Package Estimate: | 9/19/23 |
| JACOBS Submitted Project Schedule: | 10/10/23 |
| NYSED Submission & Pricing Package: | 12/15/23 |
| NYSED Approval & Bid Date: | 2/13/24 |
| Bid Opening & Award: | 3/19/24 + BOE |
| Projected Construction Start Date: | 5/1/24 |
| Projected Project Completion: | 8/25/25 |

2. High School Core Renovations

| | |
|--|-----------------------|
| SEI Concept/Schematic Pricing Package: | 11/20/23 |
| JACOBS Concept/Schematic Estimate: | to begin upon receipt |





INSPIRE

• IMAGINE




• ENGAGE



4. SCSD Revitalization Plan 2030

a. High School Schedule Sequence Tract


1. Freshman Leadership Academy @ Steinmetz

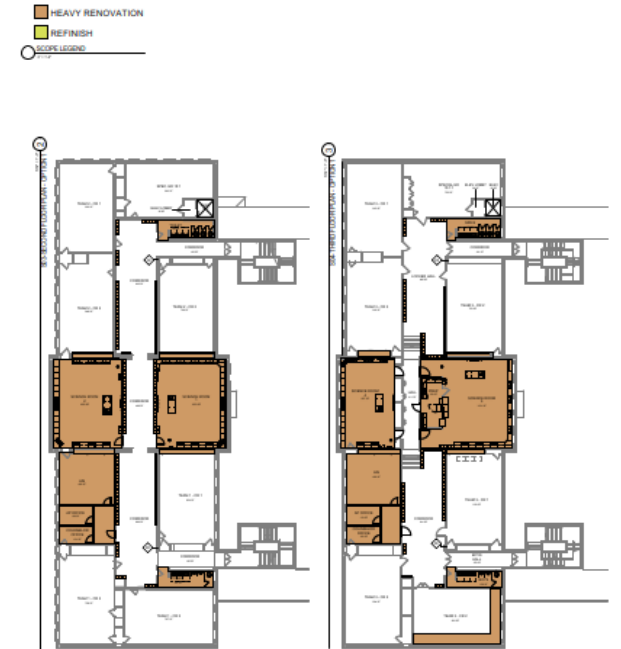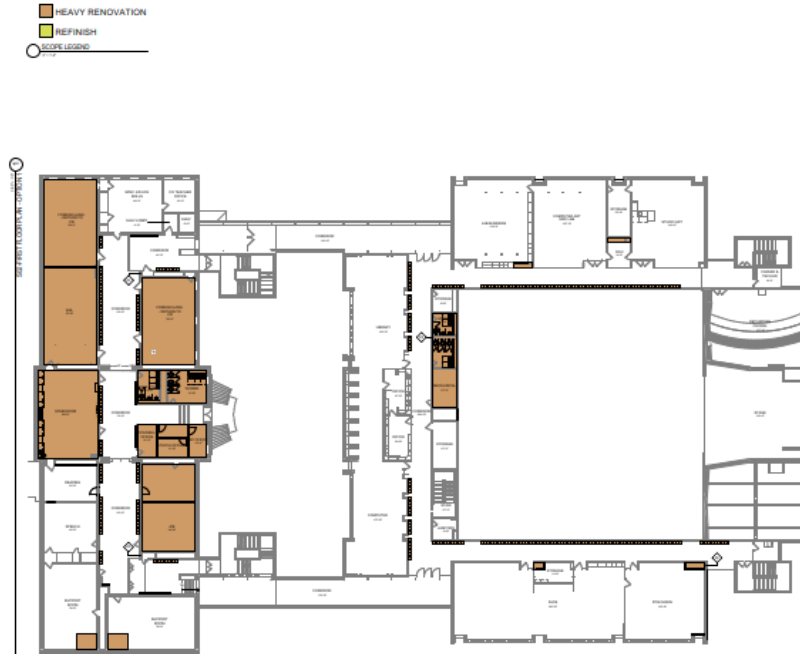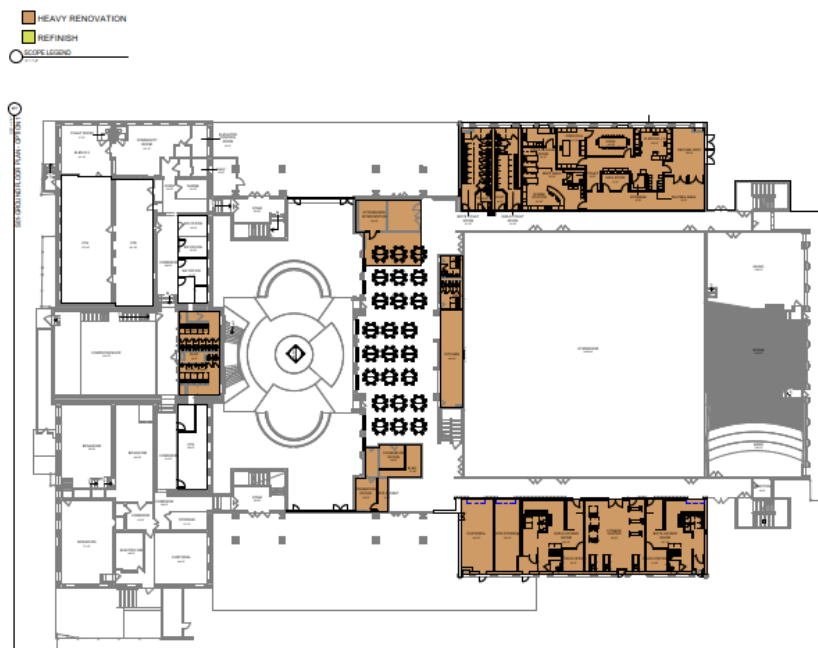

4. SCSD Revitalization Plan 2030

a. High School Schedule Sequence Tract

1. Freshman Leadership Academy @ Steinmetz

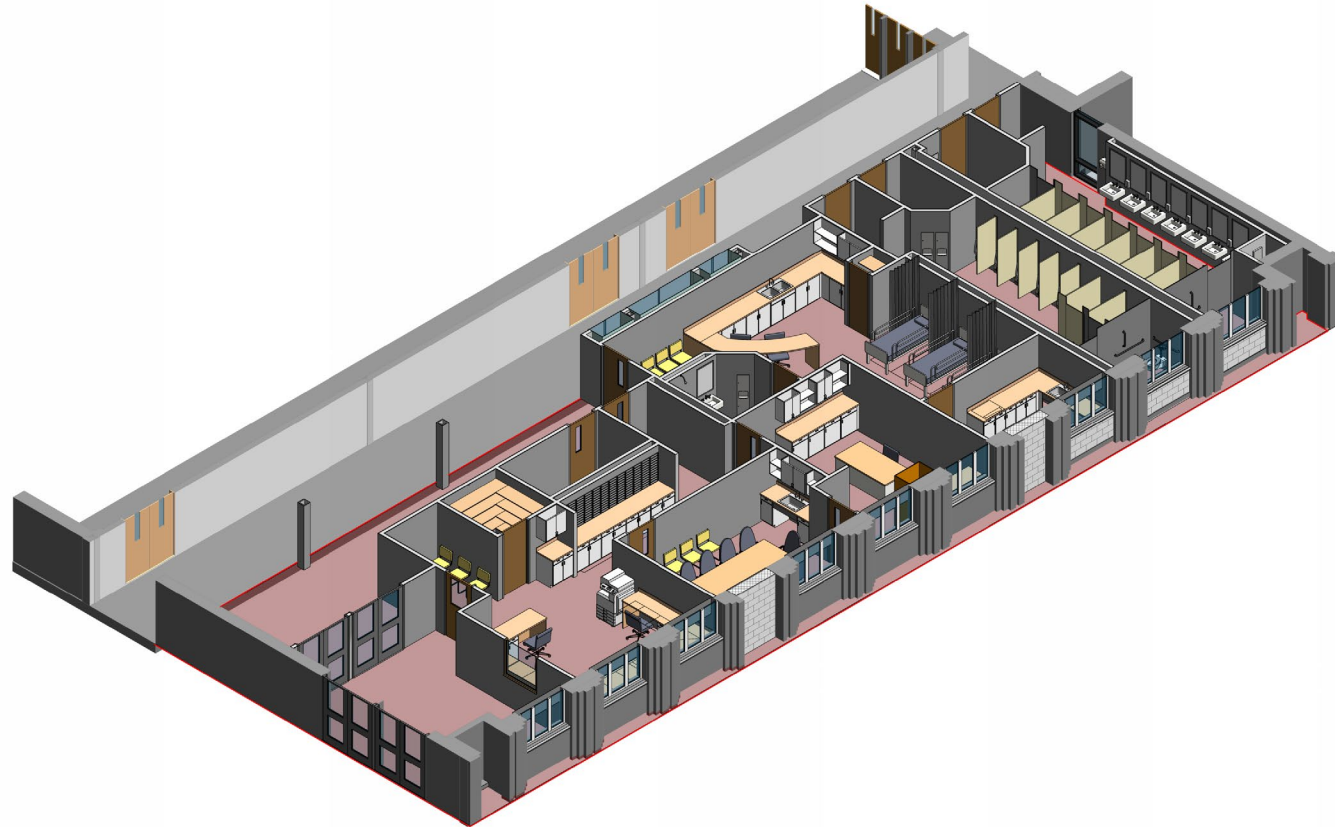


3 MAIN OFFICE & NURSE SUITE AXONOMETRIC

4. SCSD Revitalization Plan 2030

a. High School Schedule Sequence Tract

1. Freshman Leadership Academy @ Steinmetz

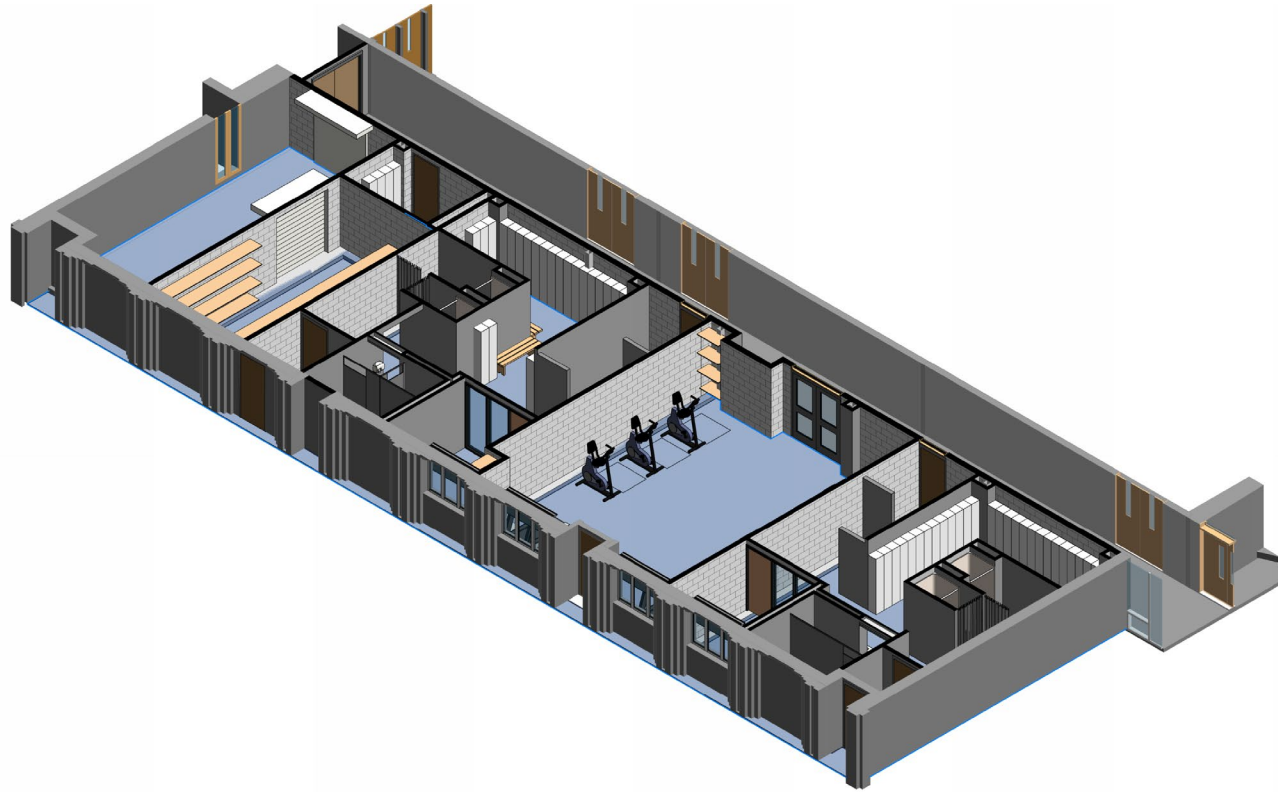

2 FITNESS SUITE - AXONOMETRIC



INSPIRE

IMAGINE

ENGAGE



4. SCSD Revitalization Plan 2030


a. High School Schedule Sequence Tract

Schenectady City School District

SCSD 2030 - Master Project Schedule Overview

11/15/2023

PRELIMINARY

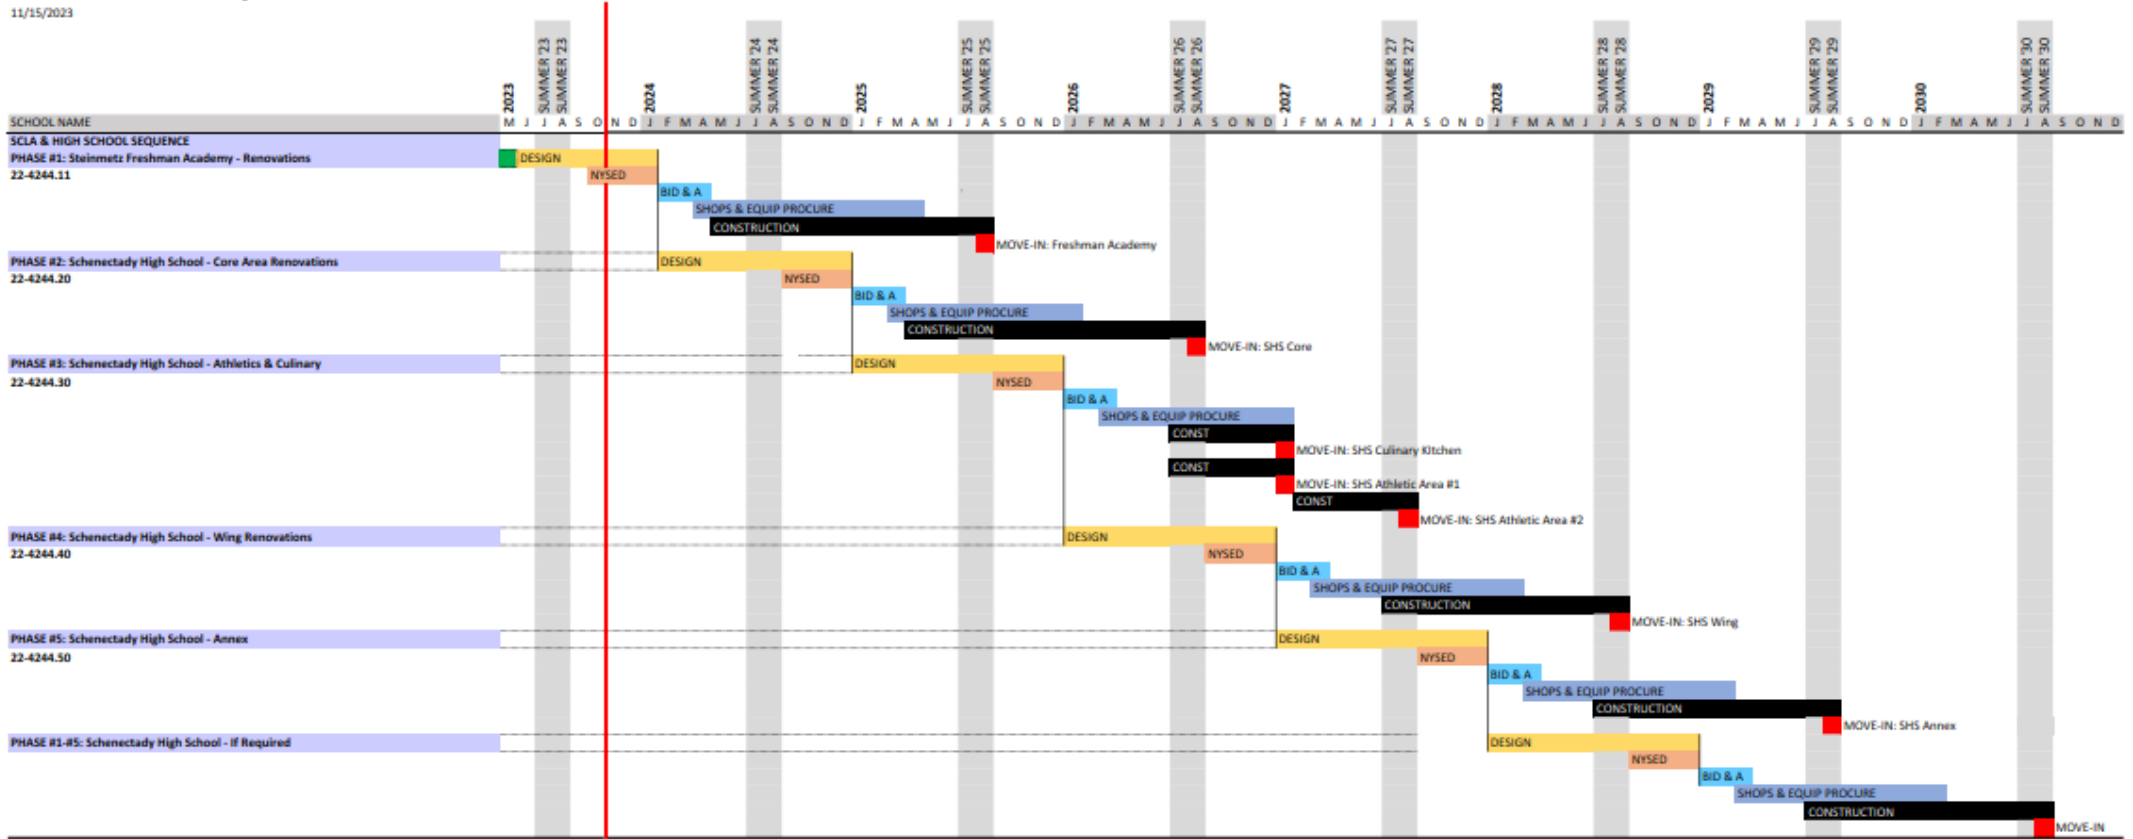

4. SCSD Revitalization Plan 2030

b. Elementary School Schedule Sequence Tract

1. Van Corlaer Elementary School

JACOBS Schematic Design Package Estimate: 10/24/23

NYSED Submission & Pricing Package: 12/15/23

NYSED Approval & Bid Date: 2/13/24

Bid Opening & Award: 4/16/24 + BOE

Projected Construction Start Date: 7/8/24

Projected Project Completion: 8/25/25

2. WC Keane Elementary School Renovations



SEI Concept/Schematic Pricing Package: 11/20/23

JACOBS Concept/Schematic Estimate: to begin upon receipt

4. SCSD Revitalization Plan 2030

b. Elementary School Schedule Sequence Tract


1. Van Corlaer Elementary School

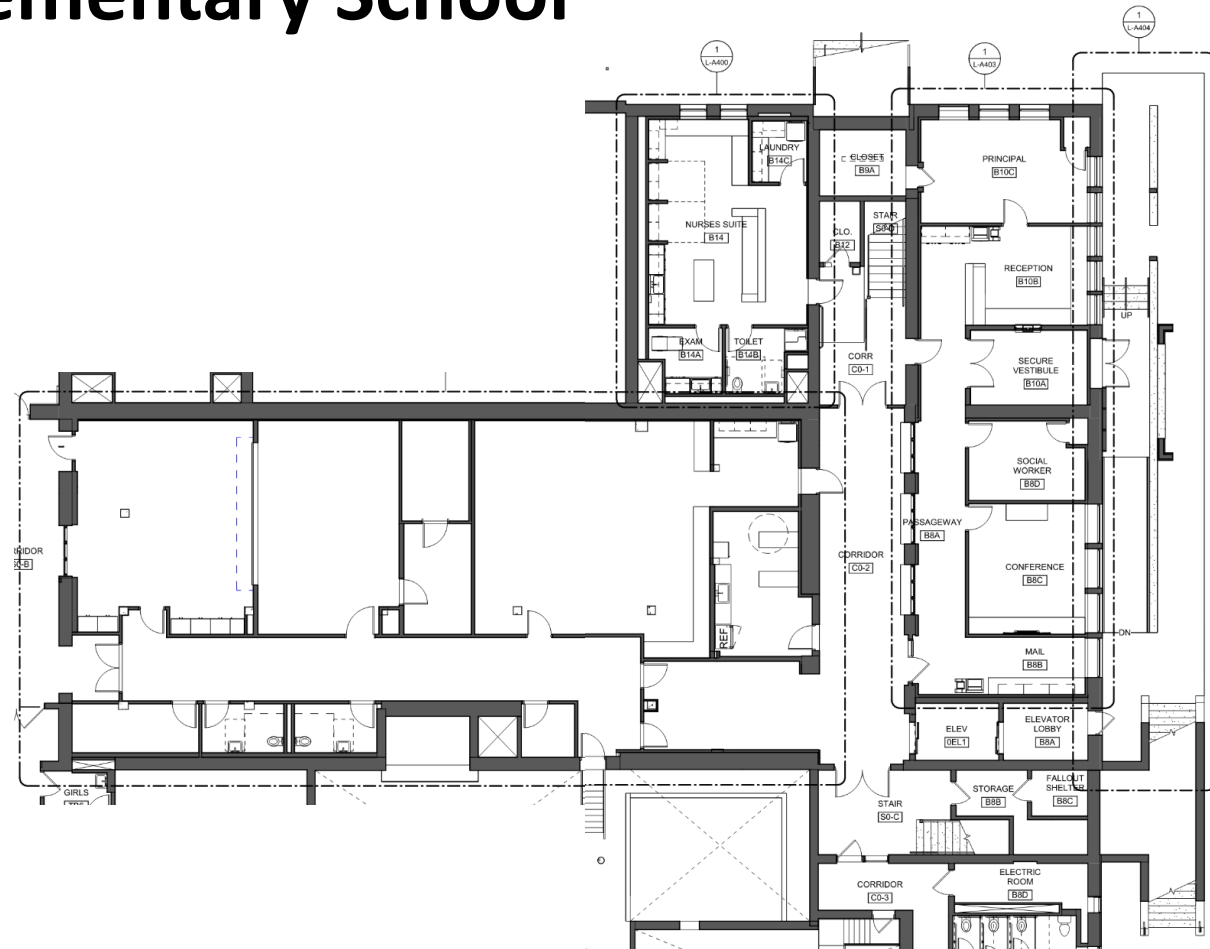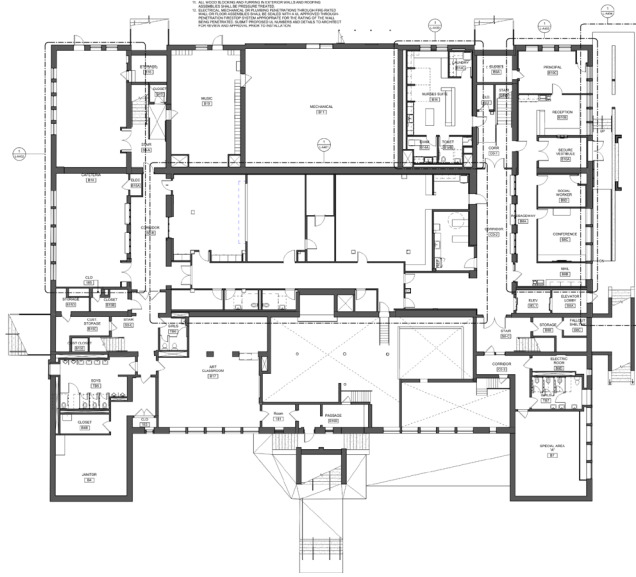

4. SCSD Revitalization Plan 2030

b. Elementary School Schedule Sequence Tract


1. Van Corlaer Elementary School

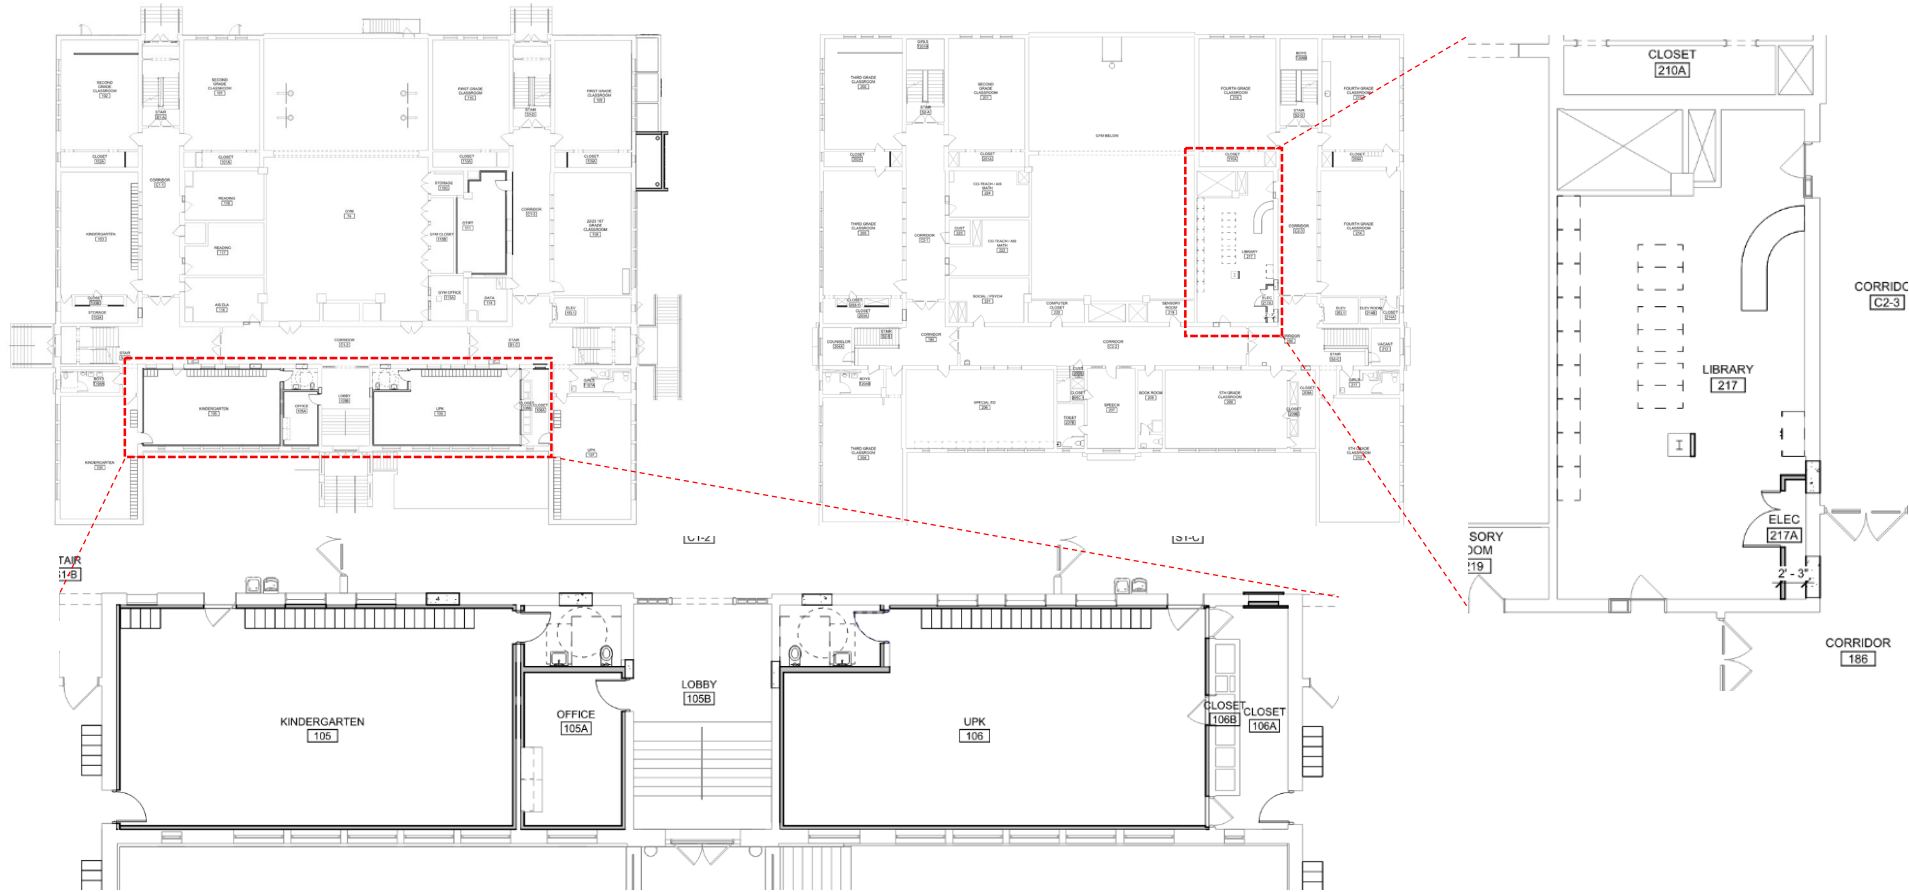

4. SCSD Revitalization Plan 2030

b. Elementary School Schedule Sequence Tract

1. Van Corlaer Elementary School

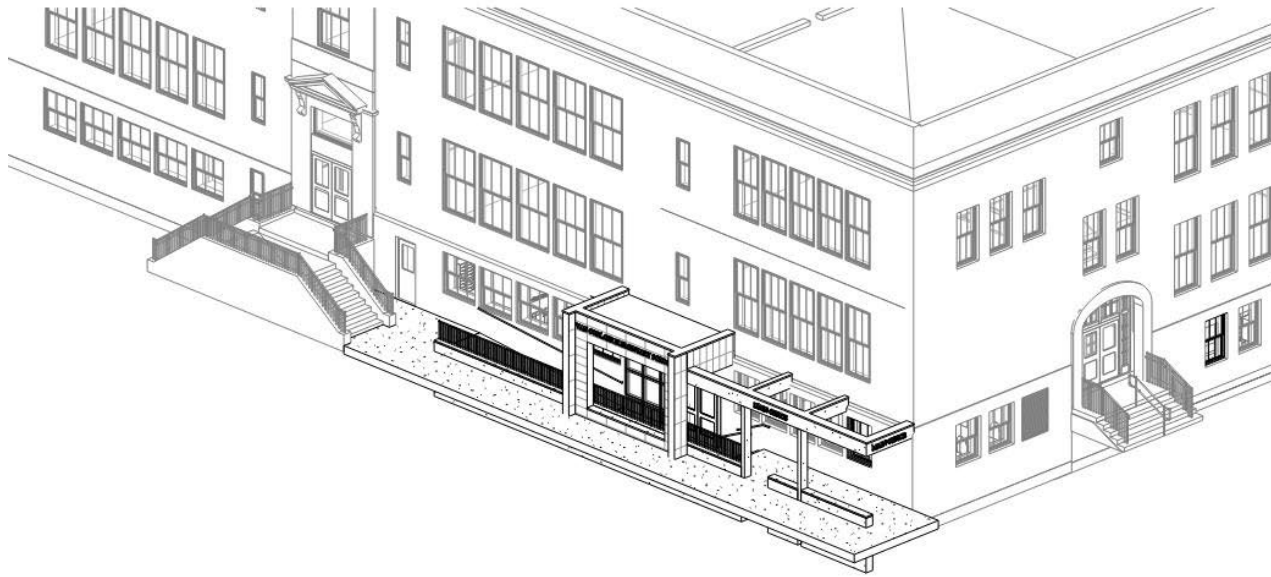



4. SCSD Revitalization Plan 2030


b. Elementary School Schedule Sequence Tract

Schenectady City School District

SCSD 2030 - Master Project Schedule Overview

11/15/2023

PRELIMINARY

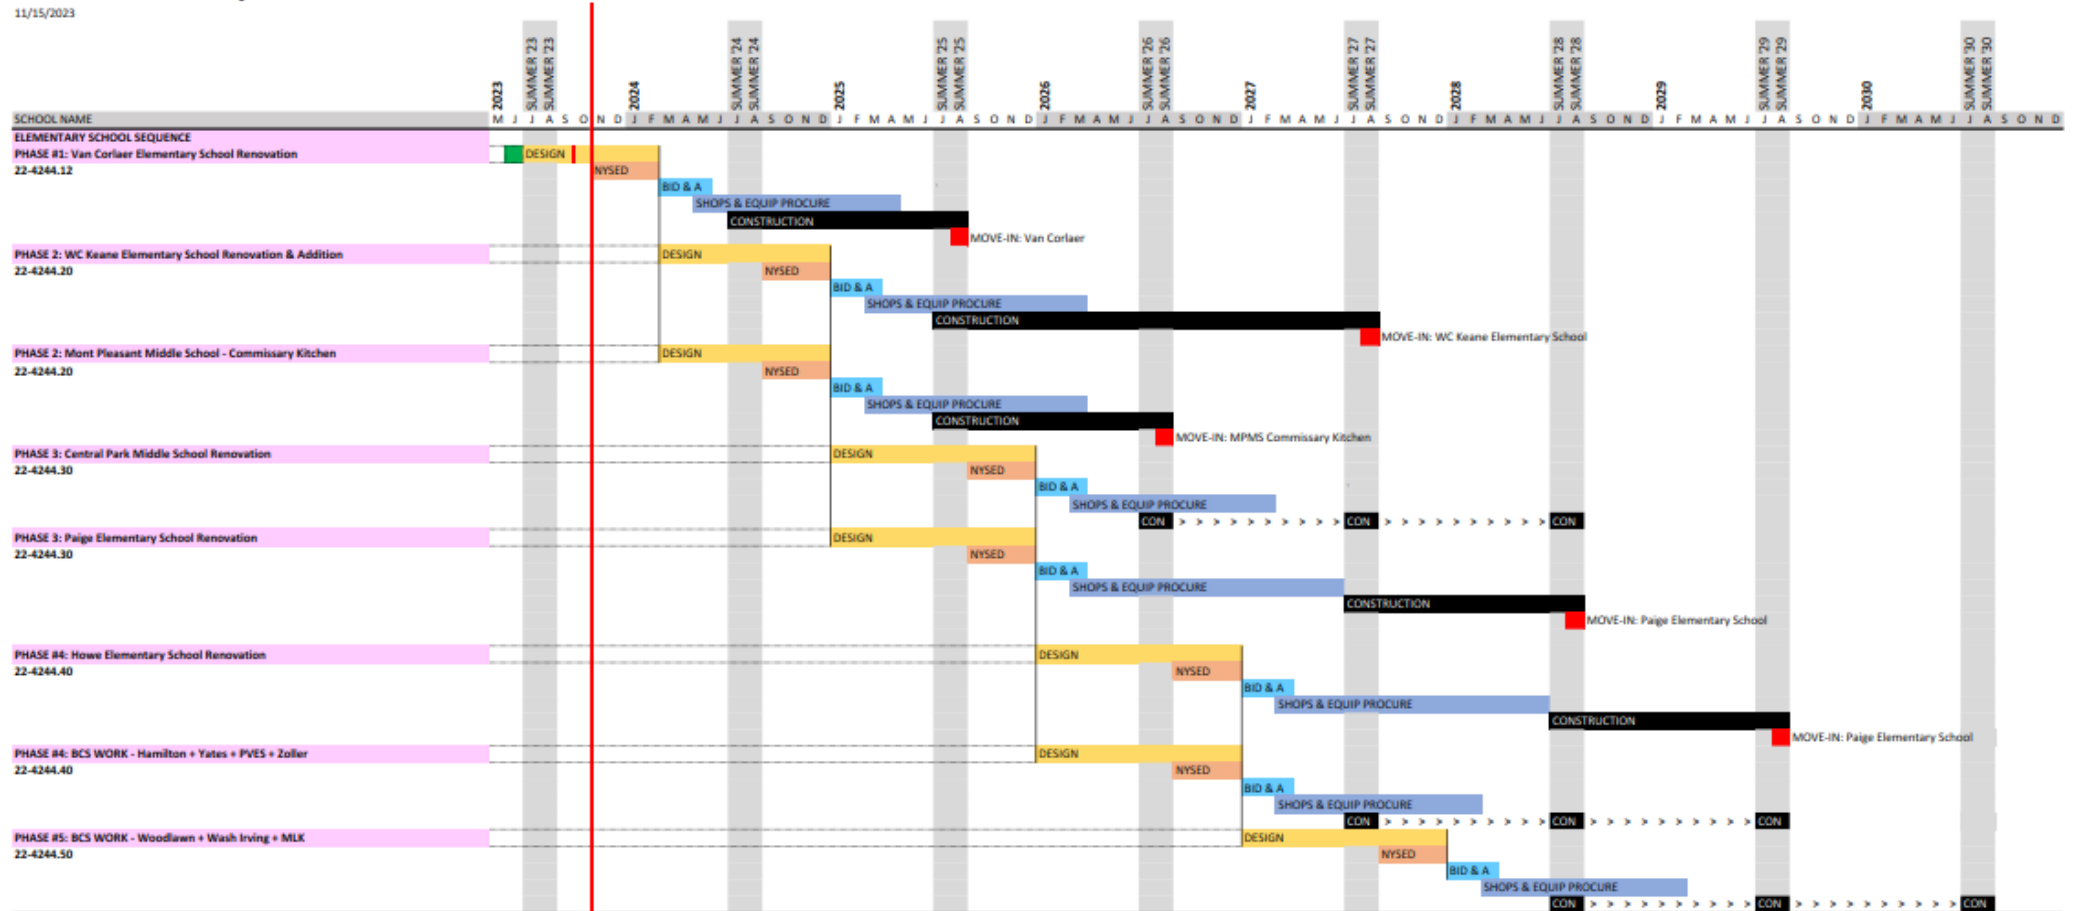

Thank you!

Questions?

ENGAGE • IMAGINE • INSPIRE

